

Record of Water Service Connection

PROJECT: LEAD SERVICE LINE REPLACEMENT PROGRAM - PHASE II

SERVICE ID: 21309 ADDRESS: 56 STREET: BYRON STREET

CONTRACTOR: C. NAUGHTON CORP DATE: JUNE 11, 2024

TYPE:

FULL (MAIN TO METER):

PARTIAL (MAIN TO CURB STOP):

PARTIAL (CURB STOP TO METER): X

MEASUREMENTS:

MAIN TO CURB STOP:

CURB STOP TO METER: 27.9'

CURB FACE TO CURB STOP: 1.7'


SERVICE DEPTH: 4.3'

WATER PRESSURE: 52 PSI

SERVICE LINE REPLACEMENT:	(YES/NO)	SIZE	MATERIAL
SERVICE LINE (MAIN TO CS):	NO	3/4"	COPPER
SERVICE LINE (CS TO METER):	YES	1"	COPPER
CORPORATION:	NO	3/4"	
CURB STOP:	YES	1"	
BALL VALVE:	YES	1"	
METER:	YES	1"	

SERIAL NUMBER: 17113618

TIES:

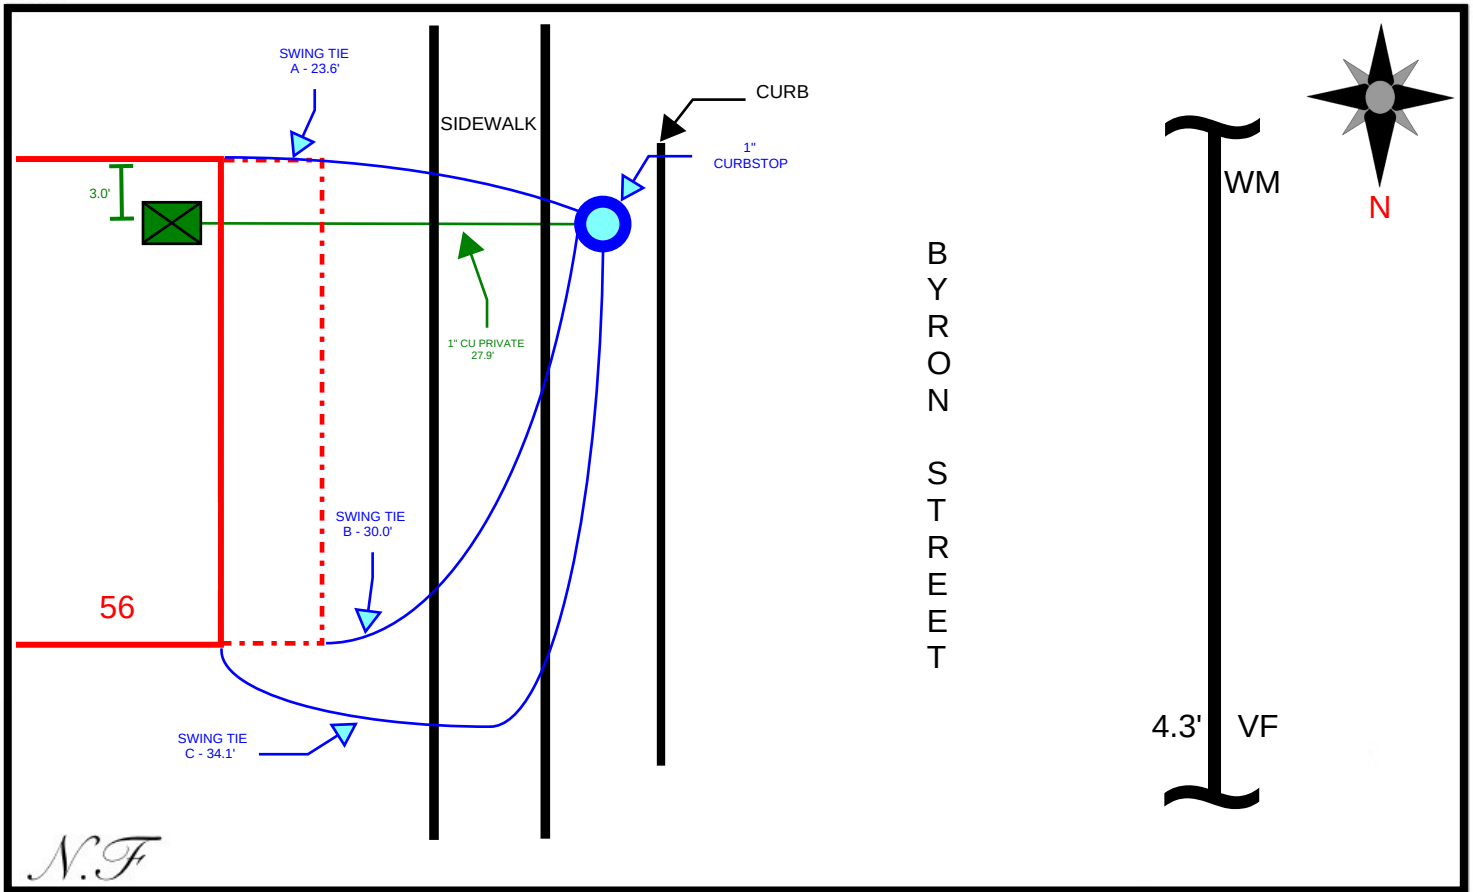

Remarks:

APPLICATION No.: 21309

TAP CLEARED 8944-0067

LOCATION: 56 Byron St.

OWNER: Esther Schultz

MEASURES: 5/8" L lead Nov.16,1927

S from Ryan St. 107.6 ft.

W from E linr Byron St. 9.4 ft.

N from S line house 2.0 ft.

11/1/89: Renewed from 1 ft. outside curb stop to a point 3 ft

Stock: 4ft. 3/4" copper tubing 1-3/4" curb stop

1 - Caldwell stop box 2-3/4 x 5/8 lead to cop adapt. xs.

11/28/00 Renewed from newly installed 8" main to property line;

Stock: 29.6 ft. - 3/4" copper tubing; 1 - 3/4" curb stop; 1 -

Caldwell stop box; 1 - 5/8" x 3/4" lead to cop. adapt. XS; 1 -

3/4" Corporation tap

DATE

BEF.

AFT.

REMARKS

[illegible]
