

APPLICATION No.: 21317 3/4" L lead

TAP CLEARED

LOCATION: 104 Bismark St.

OWNER: A. Boulet

MEASURES: 3/4"

L lead

Dec. 13, 1927

N from S line

Manila

15.4 ft.

W from E line

Bismark

6.2 ft.

S from S line

House

3.0 ft.

August 11, 1970 Renewed from 6" outside curb stop to 1' inside curb stop
 1½ ft. - 3/4" copper tubing; 1-3/4" Hays curb stop;
 2 wipe joints.

- - -

7/31/06 While installing new water main on Bismark St., cont.
 Eric Smith broke 3/4" service . Cont. renewed from a point 24.6
 ft. W x F line Bismark St. to a point 28.8 ft.

03.08.2018- Lead Service Line Replacement Program
 Contractor P. Gioioso and Sons
 Type: CU; Diameter (in) 1; Water Pressure (PSI) 60
 Distance from main to curb stop (ft) N/A
 Distance curb stop to meter (ft) 35.0
 Distance from curb face to curb stop (ft) N/A
 Depth of service (ft) 5
 Total length of new pipe installed 38.0

Curb stop replaced:

No size n/a; corporation replaced no size n/a


Ball Valve Furnished Yes Size 1:

METER HISTORY

CHARGE OUTS

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST			REMARKS

Ties:

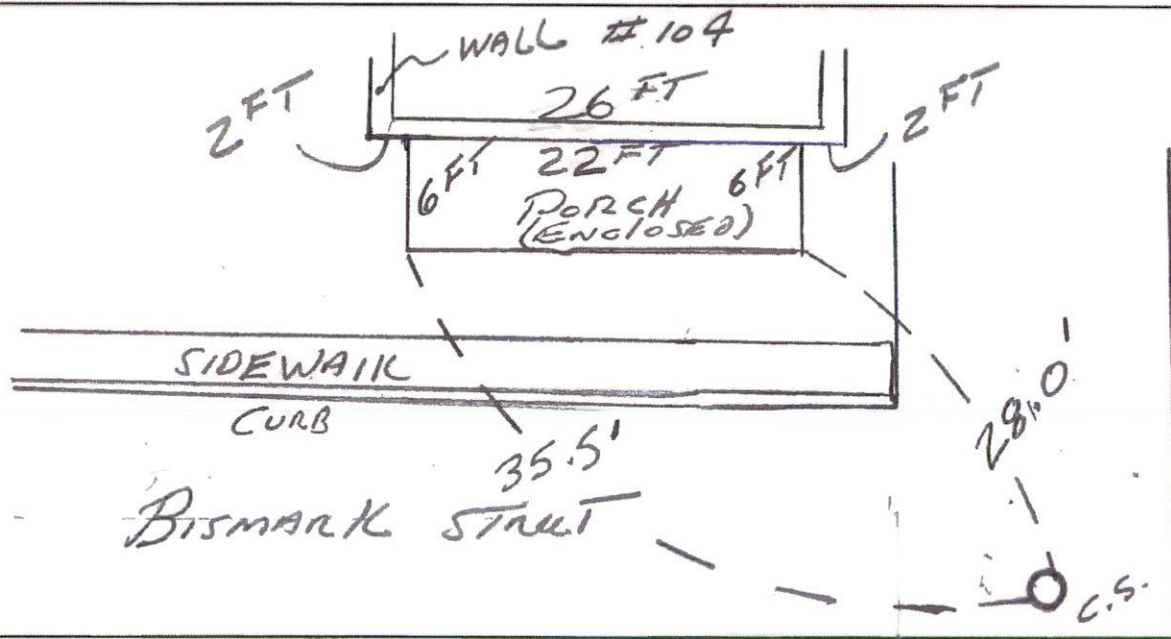

Remarks:

APPLICATION No.:

21317

TAP CLEARED

LOCATION: _____

OWNER: _____

31-313

MEASURES:

Contractor replaced existing curbstop box with new curb
stop box. Service pulled meter to curbstop. Trench
excavated in front of porch

DATE

BEF.

AFT.

REMARKS

METER HISTORY

[illegible]

CHARGE OUTS
