

APPLICATION No.: 2445

TAP CLEARED

LOCATION: 337 Orchard St

OWNER:

31-313

MEASURES: 1" Copper Service
09/27/2018 Lead Service Replacement Program
Phase 1, Contractor P Gioioso & Son
Type CU, Diameter 1in, Water pressure 100
Distance from curb stop to main (ft) N/A
Distance from curb stop to meter (ft) 7.8
Distance from curb stop to curb face (ft) 2
Depth of service (ft) 4
Total length of new pipe installed (Ft) 7.8
Curb stop replaced: NO Corporation replaced: No
Ball valve replaced: Yes size 1"

DATE

BEF.


AFT.

REMARKS

METER HISTORY

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST			REMARKS

CHARGE OUTS

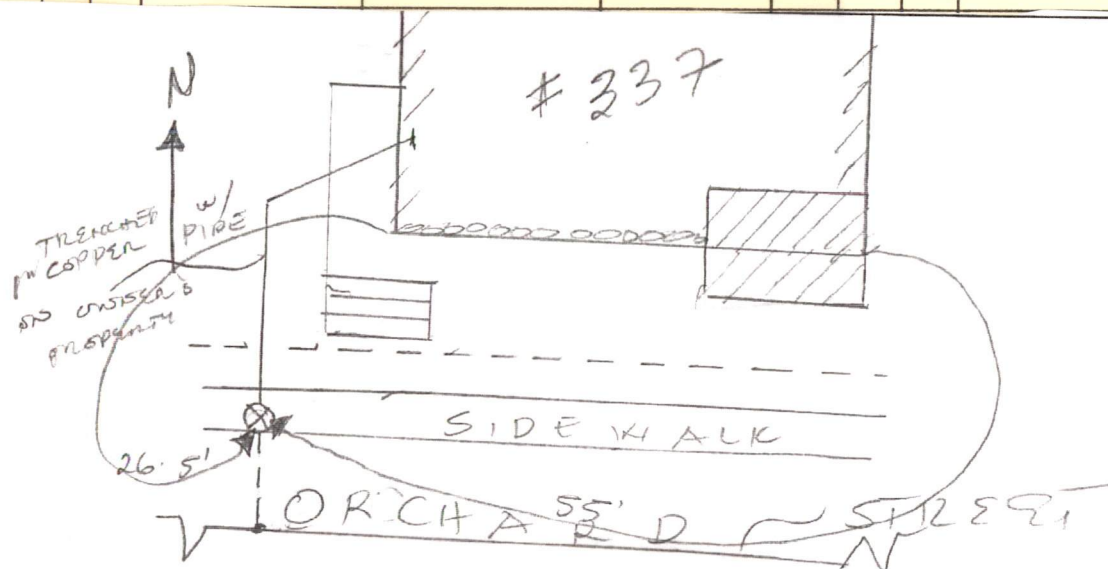

APPLICATION No.: 2445

TAP CLEARED 8703-1700 ✓

LOCATION: 337 Orchard St.

OWNER: Louis M. Pires

MEASURES: 5/8" H lead Apr. 21, 1876

S from Washington St. 175.1 ft.

E from W line Orchard St. 6.5 ft.

~~S from S line house 8.6 ft.~~

March 18, 1974 Renewed from a point 1 ft. from the curb stop to the property line.

3 ft. - 3/4" Copper tubing

2 wipe joints

— — —

Nov. 15, 1974 Renewed from 6" outside curb stop to property line.

8 ft. - 3/4" Copper tubing 3/4" curb stop

2 - 3/4" x 5/8" lead to cop.

adaptor XXS

— — —

2/18/87: Renewed from main to curb stop. Stock: 8.3 ft. 3/4" copper tubing 1-Caldwell stop box 1-1/2 x 3/4 Fig.413

Corrected & additional measure (hydrant)

S x S line house 19.3 ft.

S x hydrant 5.6 ft.

BRADBURY-WARING, INC.

[illegible]

CHARGE OUTS

[illegible]
