

APPLICATION No.: 28547

TAP CLEARED ✓

LOCATION: S.S. 110 Clifford St., E x Arlington St.

OWNER: DBA

MEASURES: 1"	Copper	11-3-71
E from E line	Arlington St.	173.0 ft.
N from S line	Clifford St.	6.0 ft.
E from W line	House	1.6 ft.
N from N line	House	21.0 ft.
Main is 18 ft. N x S line.		

1" Copper Service

09/01/2022 2022 Water main improvement program

Contractor: C. Naughton Corp.

Type CU Diameter 1"

Distance from main to curb 9.5'

Distance from curb stop to meter N/A

Distance curb face to curb stop 1.5'

Depth of Service 4.5'

Total length of new pipe installed 9.5'

Curb Stop replaced yes size 1"

Corporation replaced yes 1"

Ball Valve replaced yes N/A

Remarks: Type A - Connect to 1" Curb stop.

DATE

BEF.


AFT.

REMARKS

METER HISTORY

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST			REMARKS
2-18-72		1"	Blank						

CHARGE OUTS

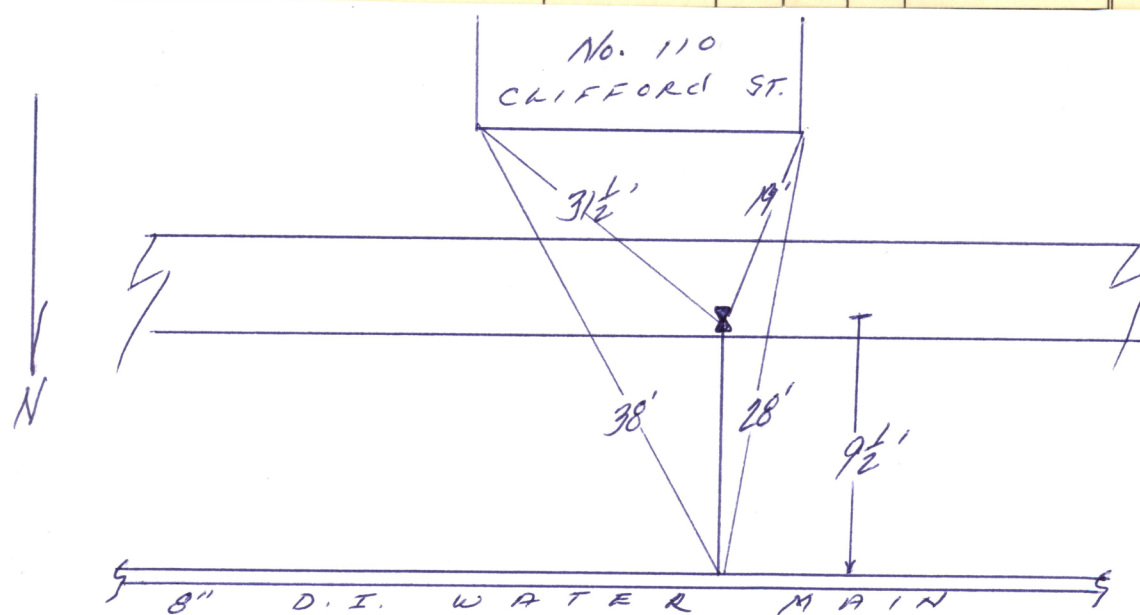

C L I F F O R D S T.
