

APPLICATION No.: 32619

LOCATION: 39-41 Clifford St. W x Acushn

OWNER: NelsonMatos Lot 233

31-313

MEASURES: 1" Copper tubing June 12, 2002

E x E line Concord St. 310.5 ft.

S x N line Clifford St. 8.8 ft.

W x E line house 6.7 ft.

Main to curb stop 24.5 ft.

1" Copper Service

08/29/2022 2022 Water main improvement program

Contractor: C. Naughton Corp.

Type CU Diameter 1"

Distance from main to curb 23'

Distance from curb stop to meter N/A

Distance curb face to curb stop 1.5'

Depth of Service 4.5'

Total length of new pipe installed 28.5'

Curb Stop replaced yes size 1"

Corporation replaced yes 1"

Ball Valve replaced yes N/A

Remarks: Type B -Connect to 3/4" Copper @ PL.

TAP CLEARED

DATE _____

BEF.


AFT.

REMARKS

METER HISTORY

CHARGE OUTS

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST		REMARKS

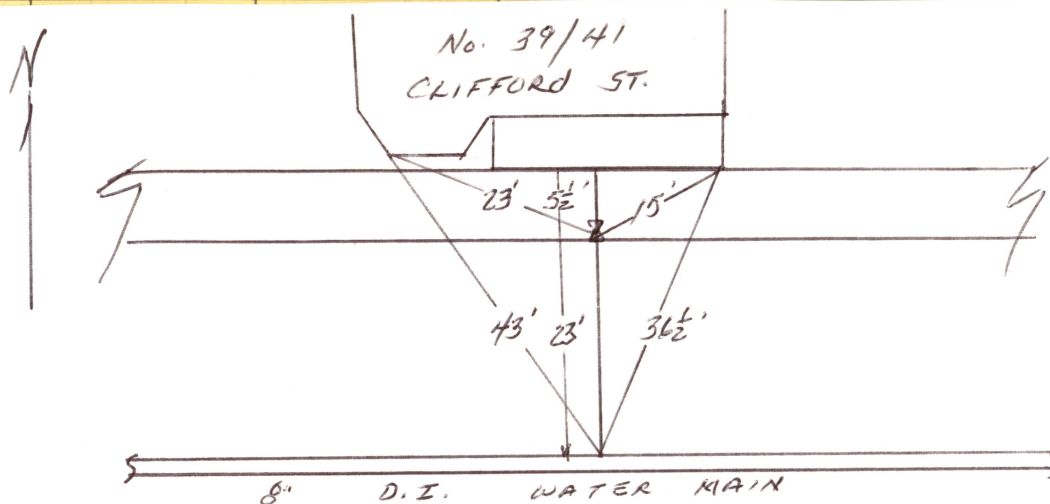

C L I F F O R D S t.

Record of Water Service Connection

PROJECT: 2022 Water Main Improvements Program New Bedford, MA

STREET: Clifford ST

HOUSE No: 39/41

Contractor: C. Naughton Corp.

Date: 8-29-22

Type: CU

Diameter (in):

1

Distance from main to curb stop (ft):

23'

Distance curb stop to meter (ft):

-

Distance from curb face to curb stop (ft):

1 1/2'

Depth of Service (ft):

4 1/2'

Total length of new pipe installed (ft):

28 1/2'

Curb Stop Replaced: Yes

Size (in):

1

Corporation Replaced: Yes


Size (in):

1

Ball Valve Replaced:

Size (in):

Ties:

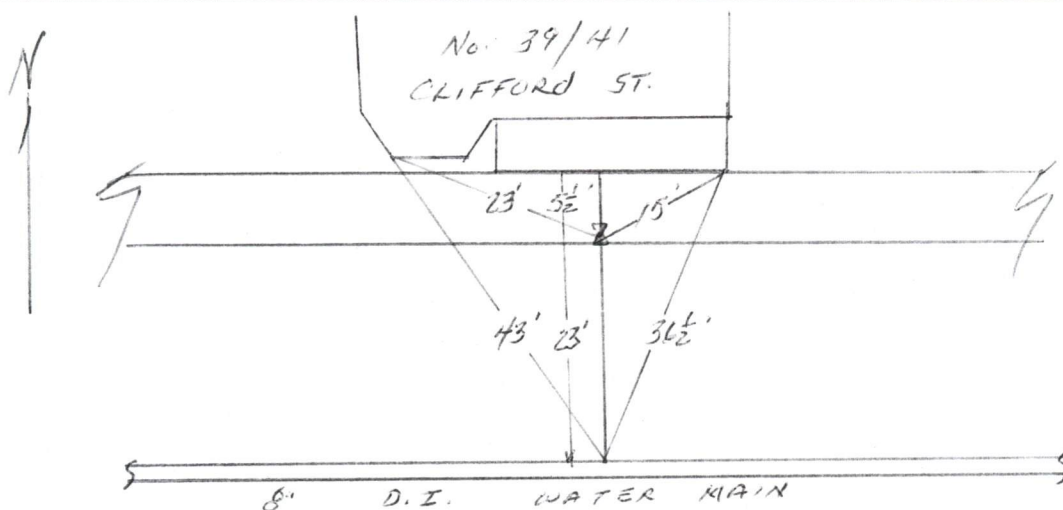

CLIFFORD ST.

Remarks:

TYPE B - CONNECT TO 3/4" COPPER @ R
