

APPLICATION No.: 3280

LOCATION: 46 Oak St

TAP CLEARED

OWNER:

31-313

MEASURES: Dec. 4, 1878

W X E Line Clay St 8.5 ft

N X S Line Oak St 6.5 ft

E X W Line Body of House 4.7 ft

1" Copper Service

06/18/2018 Lead Service Replacement Program

Phase 1, Contractor P Gioioso & Son

Type CU, Diameter 1in, Water pressure 70

Distance from main to curb stop (Ft) 7

Distance from curb stop to meter (ft) 47.6

Distance from curb face to curb stop (ft) 1.4

Depth of service (ft) 4.5

Total length of new pipe installed (ft) 47.6


Curb stop replaced: NO Size 3/4"

Corporation replaced: NO Size 3/4"

Ball valve replaced: YES size 1"

Remarks: 3/4 - 1 union installed 1.0 ft outside curb stop

[illegible]

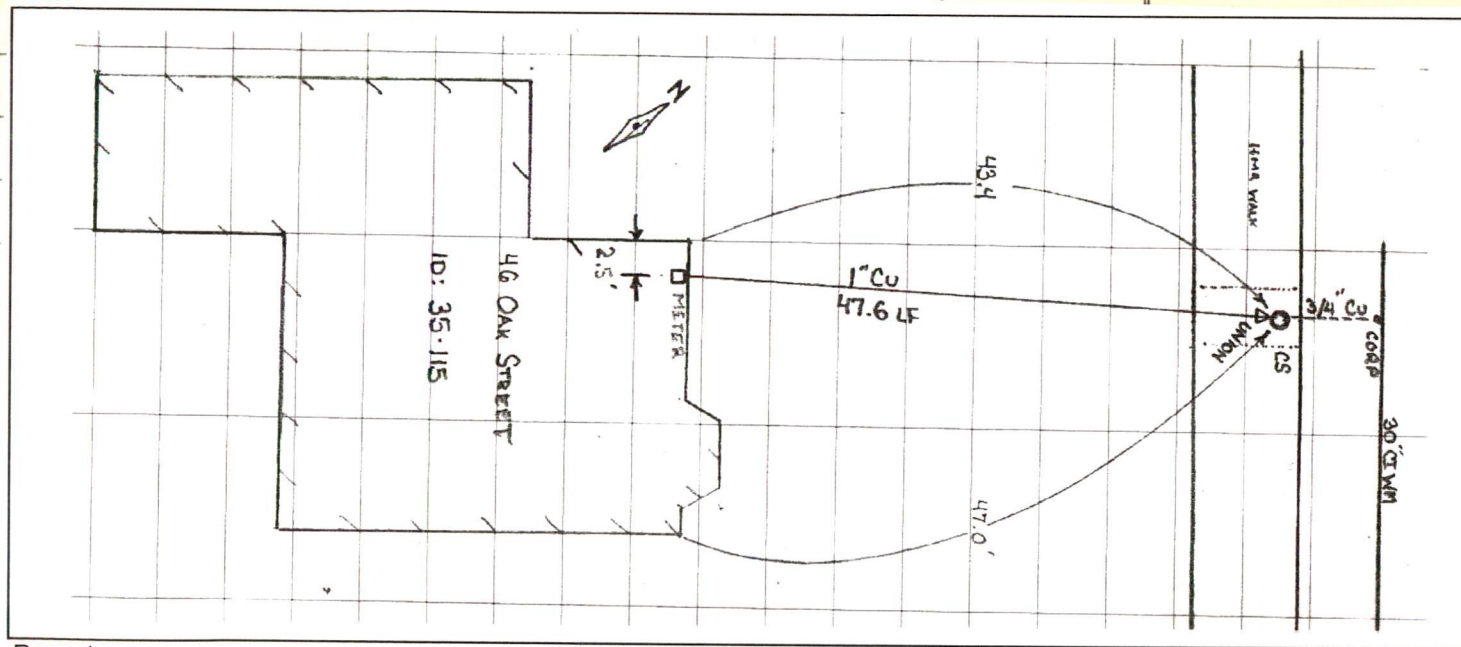

Remarks:

[illegible]
