



TAP CLEARED

DATE	BEF.	AFT.	REMARKS
------	------	------	---------

Lot #123

MEASURES: 4"

D.I.

July 26, 2006

FIRE SUPPLY

Measures of 4" Gate Valve:

W x W line Acushnet Ave.

50.0 ft.

N x S line building

13.0 ft.

E x hydrant

8.0 ft.

Nelson Cardoso Cont. supplied & installed:

1 - 8" x 8" x 4" tapping sleeve

1 - 4" gate valve

15 ft. 4" DI Pipe

METER HISTORY

[illegible]


CHARGE OUTS

1

465

7/26/06

Nelson Cardoso Contractor
Installed New Fire Supply
for 1053 ACUSHNET AVE
1623

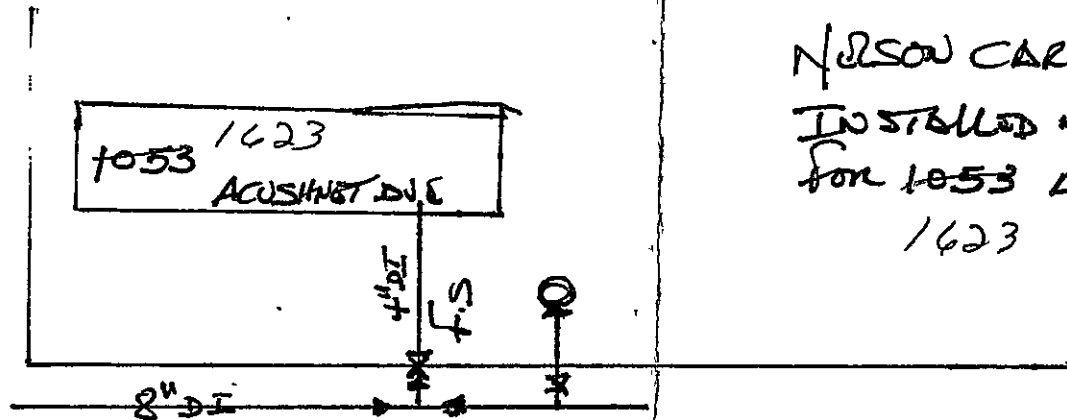

ACUSHNET AVE

EARL ST

New fire supply on S.S. EARL ST
50' W.W LINE ACUSHNET AVE
1- 8" x 8" x 4" TAPPING SLAVE
1- 4" GATE VALVE
15' - 4" DI PIPE

GATE VALVE MEASURE:
W.W LINE ACUSHNET AVE - 50' 0"
NKS LINE BUILDING - 13' 0"
E x HYD - 8' 0"

F. Bento
7/26/06

