

4107

APPLICATION No.:

TAP CLEARED

LOCATION: 266 Orchard St

OWNER:

31-313

MEASURES:

Dec 10, 1881

S X Dartmouth St

86.2 ft

W X E Line Orchard St

6.9 ft

N X S Line House

15.3 ft

1" Copper Service

09/10/2018 Lead Service Replacement Program

Phase 1, Contractor P Gioioso & Son

Type CU, Diameter 1in, Water pressure 80

Distance from main to curb stop (ft) 21

Distance from curb stop to meter (ft) 16.8

Distance from curb face to curb stop (ft) 3

Depth of service (ft) 4

Total length of new pipe installed (Ft) 16.8

Curb stop replaced: No size 3/4"

Corporation replaced: NO size 3/4"

Ball valve replaced: Yes size 1'

Remarks: 1-3/4 union installed 1 lf outside curb stop

DATE

BEF.

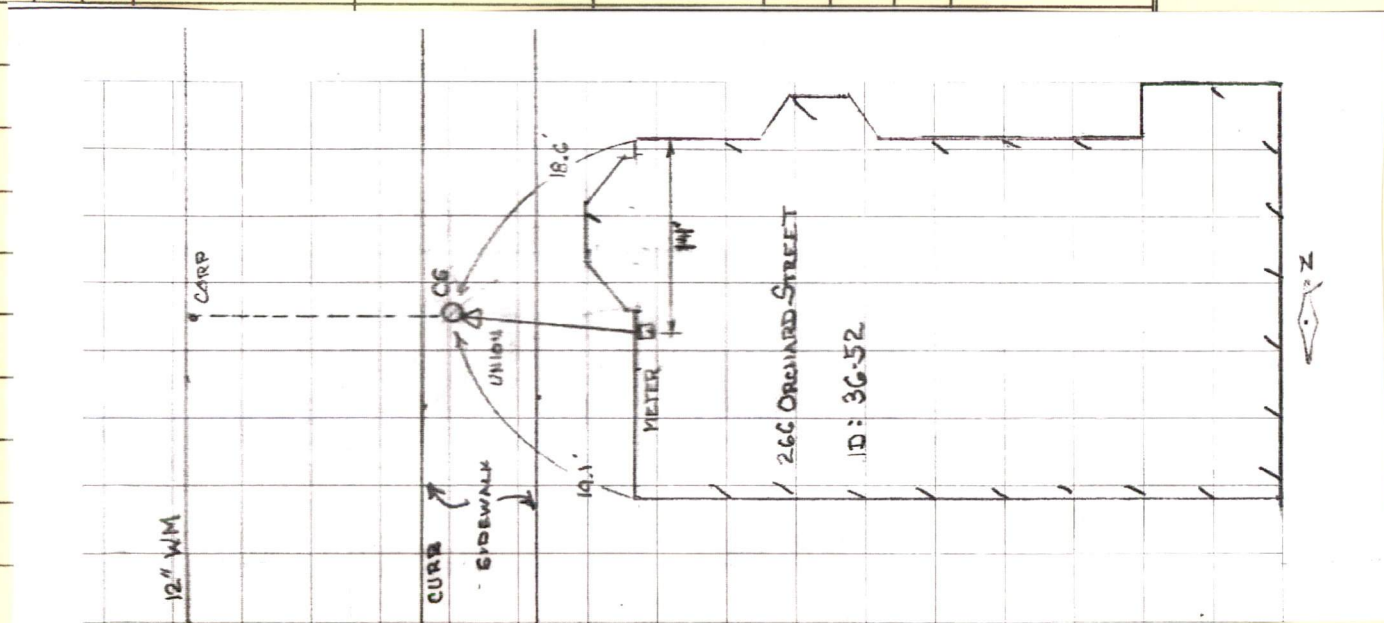
AFT.

REMARKS

5/5/06

6/14/06 Ream

10/12/06

[illegible][illegible]
