

APPLICATION No.: 4548

## TAP CLEARED

LOCATION: 72 Delano St

OWNER:

31-313

MEASURES: Sept 24, 1883

E X Acushnet Ave 122.1 ft

N X S line Delano St 6.7 ft

W X E line House 5.0 ft

1" Copper Service

01/14/2019 Lead Service Line Replacement Program

Phase 1, Contractor P Gioioso &amp; Son

Type CU Diameter 1in Water pressure 90

Distance from main to curb stop (ft) 9

Distance from curb stop to meter (ft) 25

Distance from curb face to curb stop (ft) 1.5

Depth of service (ft) 5

Total length of new pipe installed (ft) 34

Curb stop replaced: yes size 1"

Corporation replaced: yes size 1"

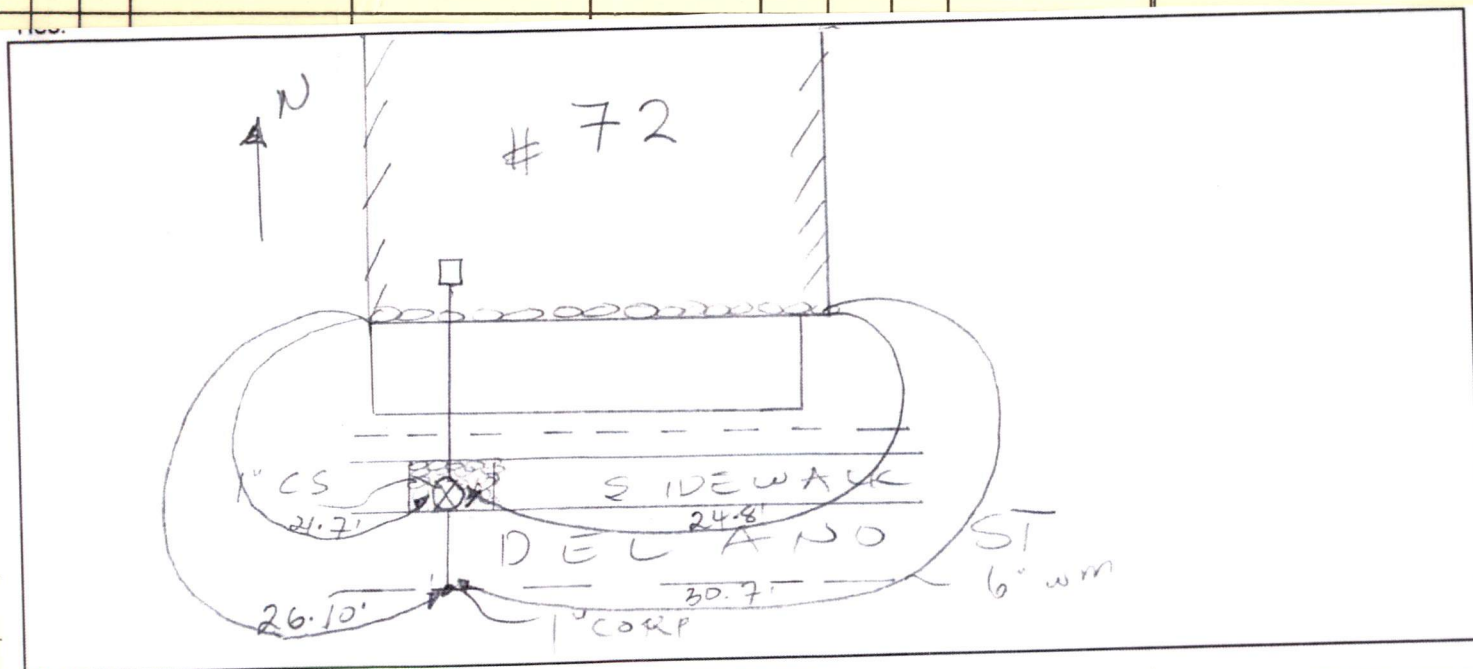
Ball valve furnished: yes size 1"

DATE

BEF.

AFT.

REMARKS

[illegible][illegible]
