

APPLICATION No.: 5542

## TAP CLEARED

LOCATION: 35 Mosher St

OWNER:

31-313

MEASURES: June 16, 1887

W X County St 327.2 ft

S X N Line Mosher St 7.2 ft

E X W Line House 1.8 ft

1" Copper Service

07/30/2019 Lead Service Line Replacement Program

Phase 1, Contractor P Gioioso &amp; Son

Type CU, Diameter 1in, Water pressure 100

Distance from main to curb stop (ft) 26.9

Distance from curb stop to meter (ft) 14

Distance from curb face to curb stop (ft) 2.0

Depth of service (ft) 4.0

Total length of new pipe installed (ft) 26.9

Curb stop replaced: yes size 1"

Corporation replaced: yes size 1"

Ball valve replaced: no size 3/4"

Remarks: Existing corp abandoned where shown

1-3/4" union installed 1FT outside curb stop

DATE

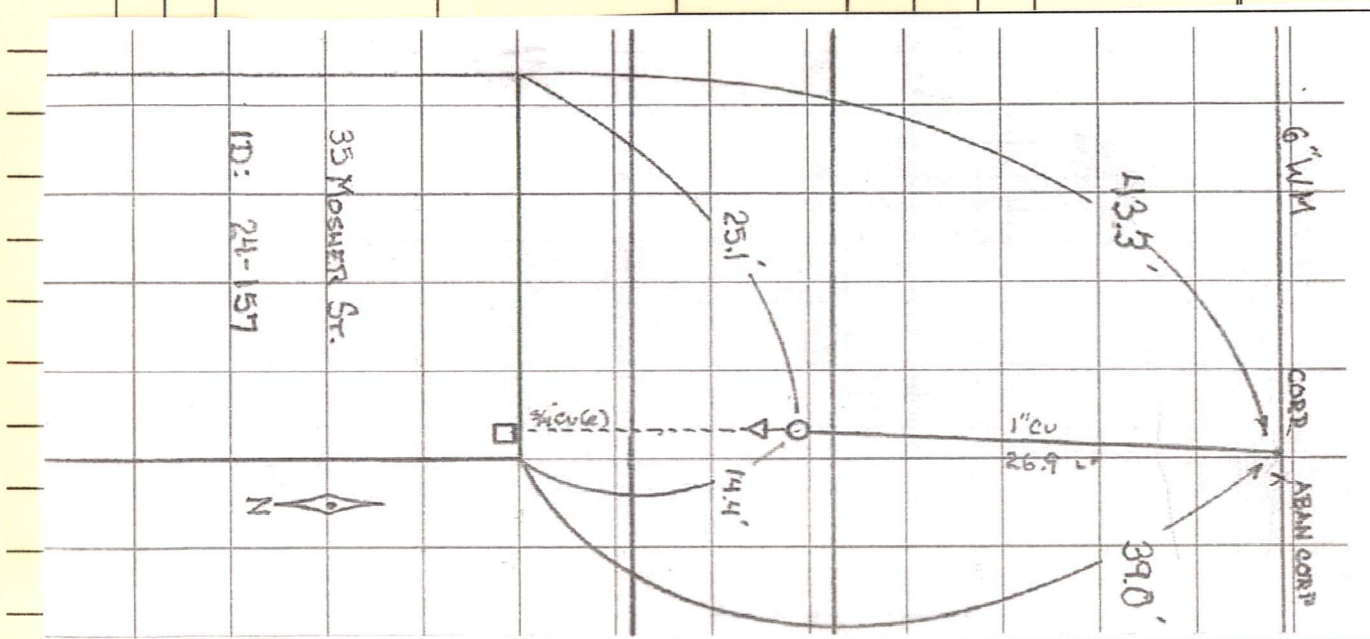
BEF.

AFT.

REMARKS

[illegible]

### CHARGE OUTS

[illegible]
