

APPLICATION No.: 5694

TAP CLEARED

LOCATION: 52 Oak St

OWNER:

31-313

MEASURES Nov 8, 1887

W X Clay St

49.6 ft

N X S Line Oak St

6.8 ft

## E X W Line House

7.0 ft

1" Copper Service

06/21/2018 Lead Service Replacement Program

Phase 1, Contractor P Gioioso & Son

Type CU, Diameter 1in, Water pressure 71

Distance from main to curb stop (Ft) 7.8

Distance from curb stop to meter (ft) 34.8

Distance from curb stop to curb face (ft) 1.7

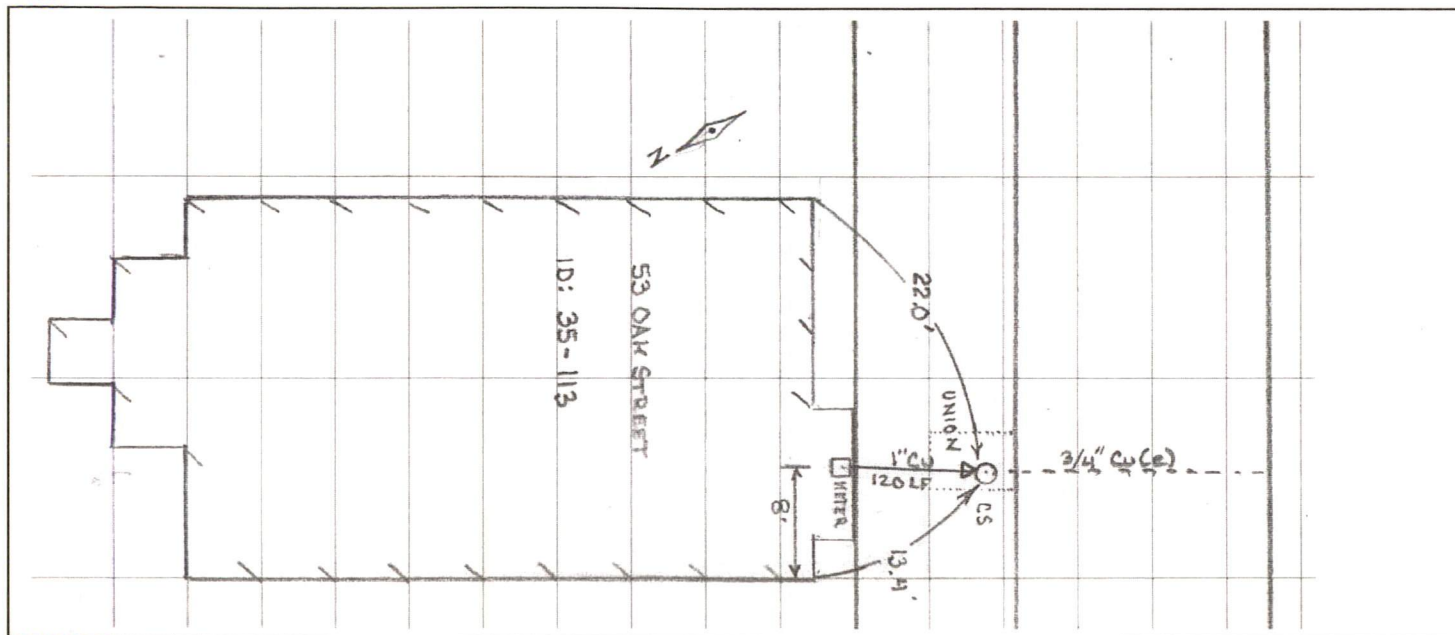
Depth of service (ft) 3.8

Total length of new pipe installed (ft) 42.6

Curb stop replaced: Yes size 1"

Corporation replaced: Yes size 1"

Ball valve replaced: Yes size 1"

[illegible][illegible]

---

---

---

---

[illegible]
