

APPLICATION No.: 5758

TAP CLEARED

LOCATION: 130 Division St

DATE

BEF.

AFT.

REMARKS

OWNER:

09/16/2004 Ream

31-313

MEASURES: April 13, 1888

W X County St 278.2 ft

N X S line Division St 7.0 ft

W X E line House 10.0 ft

1" Copper Service

08/08/2019 - Lead Service Line Replacement Program

Phase 1, Contractor P. Gioioso & Son

Type CU, Diameter 1in, Water pressure 90

Distance from main to curb stop (ft) 8

Distance from curb stop to meter (ft) 25.8

Distance from curb face to curb stop (ft) 2.5

Depth of service (ft) 4.3

Total length of new pipe installed (ft) 25.8

Curb stop replaced: no size 3/4"

Corporation replaced: no size 3/4"


Ball valve furnished: yes size 1"

Remarks: 1-3/4" union installed 1 ft outside curb stop

METER HISTORY

DATE	SET OUT	MAKE	NUMBER	READING	TEST	REMARKS
------	---------	------	--------	---------	------	---------

CHARGE OUTS

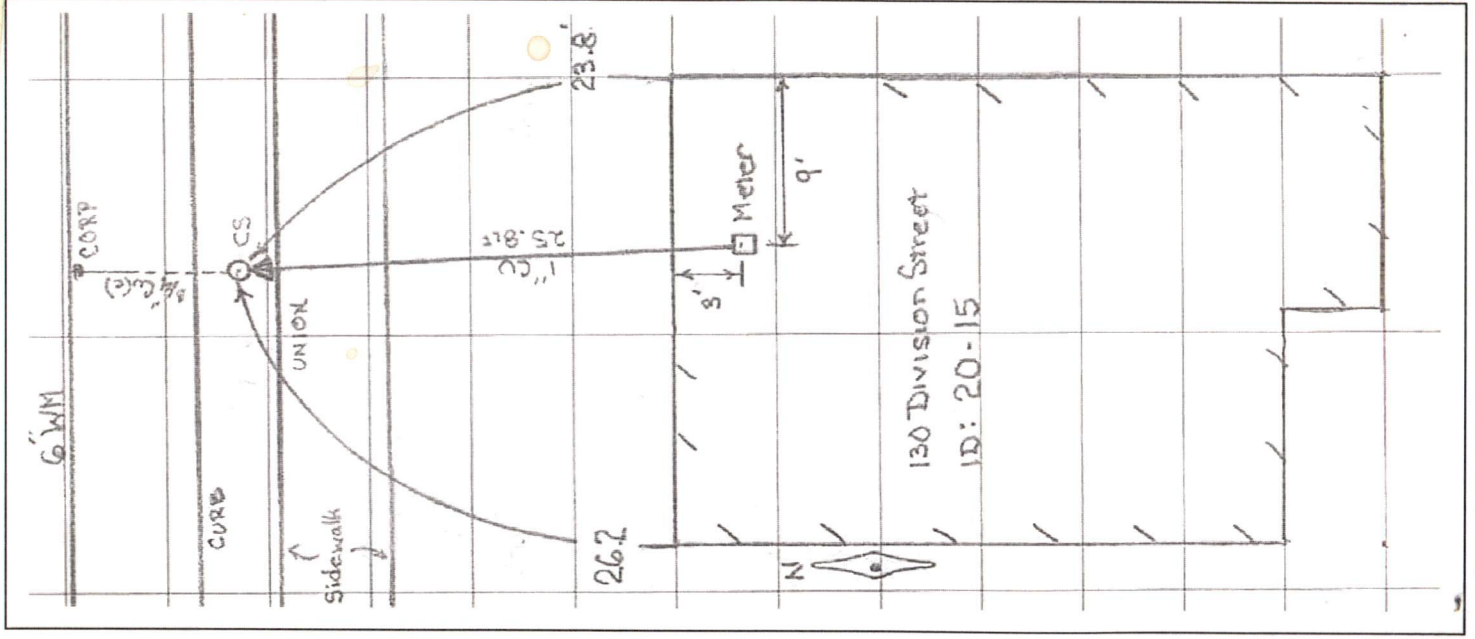

Ties:
