

✓ APPLICATION No.: 6146

LOCATION: 23 Welcome St

OWNER:

31-313

MEASURES:	E X French Ave	174.2 ft
	S X N Welcome St	8.8 ft
	W X E House	11.9 ft

1" Copper Service 4/12/2019

Lead Service Line Replacement Program

Phase 1, Contractor P Gioioso & Son

Type CU, Diameter 1in, Water pressure 100

Distance from main to curb stop (ft) 24.3

Distance from curb stop to meter (ft) 15

Distance from curb face to curb stop (ft) 1.5

Depth of service (ft) 4

Total length of new pipe installed (ft) 24.3

Curb stop replaced: Yes size 1"

Corporation replaced: Yes size 1"

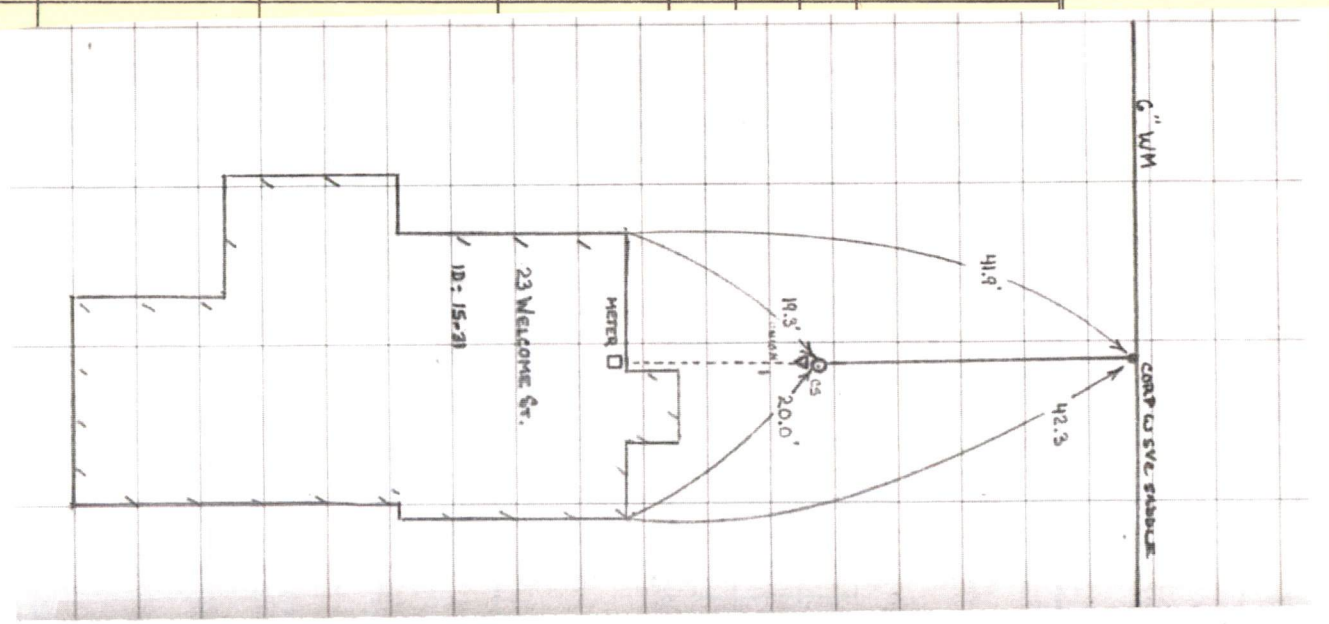
Ball valve replaced: no size 3/4"

Remarks: service saddle with 1inch corporation installed at 6 inch main	
--	--

1-3/4" union installed 1 ft outside curb stop

[illegible]

CHARGE OUTS

[illegible]
