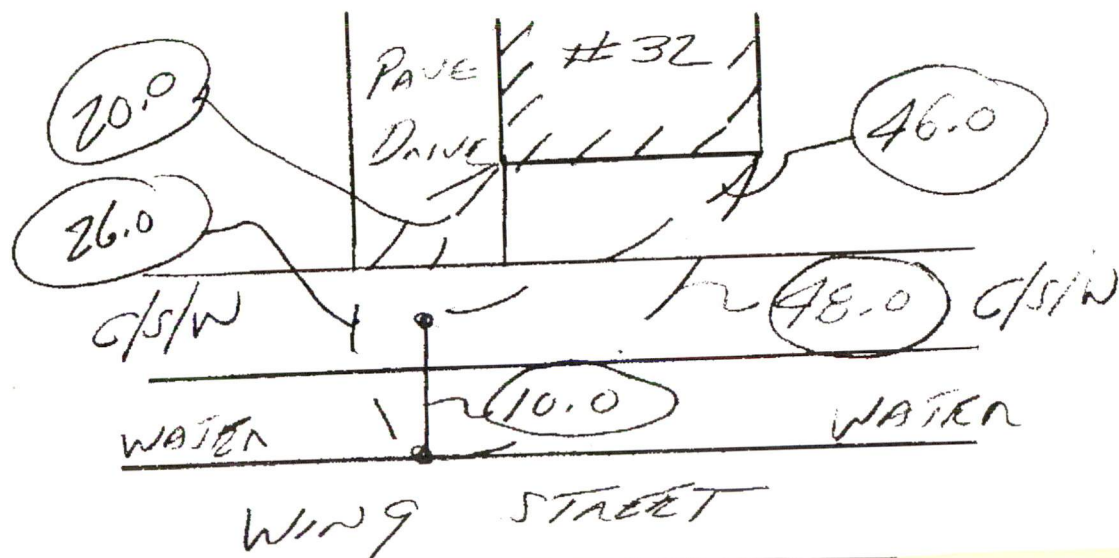


8033

OWNER:

31-313

MEASURES: 1" Copper Service 8/13/2018
Lead Service Line Replacement Program
Phase 1, Contractor P Gioioso & Son
Type CU, Diameter 1in, Water pressure 70
Distance from main to curb stop (Ft) 10
Distance from curb stop to meter (ft) N/A
Distance from curb face to curb stop (ft) 2
Depth of service (ft) 3.5
Total length of new pipe installed (ft) 10
Curb stop replaced: Yes size 1"
Corporation replaced: Yes size 1"
Ball valve replaced: No size 3/4"

[illegible]

APPLICATION No.: 8033

TAP CLEARED

LOCATION: 34 Wing

OWNER: Pacheco

MEASURES: 5/8"

W from	Pleasant	105.6 ft.
N from S	Wing	6.9 ft.
E from E	house	4.2 ft.

Change over to 3/4 from curb to cella

 Jan. 17, 1955 Renewed from main to a point $\frac{1}{2}$ ft. inside curb stop.
 7 $\frac{1}{2}$ ft. of 3/4" copper tubing 1 3/4" cop. to I.f.cplg.
 1 wipe joint 1 copper curb stop

Feb. 12, 1970 Renewed from curb stop to inside the cellar.
 22 ft. of 3/4" copper tubing (15 ft. inside)

5/2/94: Renewed from 2.5ft outside curb stop to curb stop
 Installed 3/4 curb stop 2.5ft outside of stop
 Stock: 2.5ft 3/4" copper tubing 2-3/4" curb stop
 1-Caldwell stop box
 =====

1/4/08 - Renewed from main to a point 2 ft

2 ft - 3/4" copper tubing; 1 - 3/4" cop to cop cplg. comp; 1 - 3/4"
 Corporation tap. 1 - 8" x 3/4" saddle Foreman: Dana Farland

DATE

BEF.

AFT.

REMARKS

1-17-55

Reamed

5-2-94

241704797

[illegible]

CHARGE 'OUTS'
