

APPLICATION No.: 8443

LOCATION: 34 Oak St

TAP CLEARED

OWNER:

31-313

Dec 24, 1895

MEASURES:

E X Clay St

94.7 ft

N X S Line Oak St

7.3 ft

E X W Line House

9.2 ft

1" Copper Service

06/19/2018 Lead Service Replacement Program

Phase 1, Contractor P Gioioso & Son

Type CU, Diameter 1in, Water pressure 70

Distance from main to curb stop (Ft) 8.2

Distance from curb stop to meter (ft) 16

Distance from curb face to curb stop (ft) 1.5

Depth of service (ft) 3.8

Total length of new pipe installed (ft) 24.2

Curb stop replaced: Yes size 1"

Corporation replaced: Yes size 1"

Ball valve replaced: Yes size 1"

DATE

BEF.

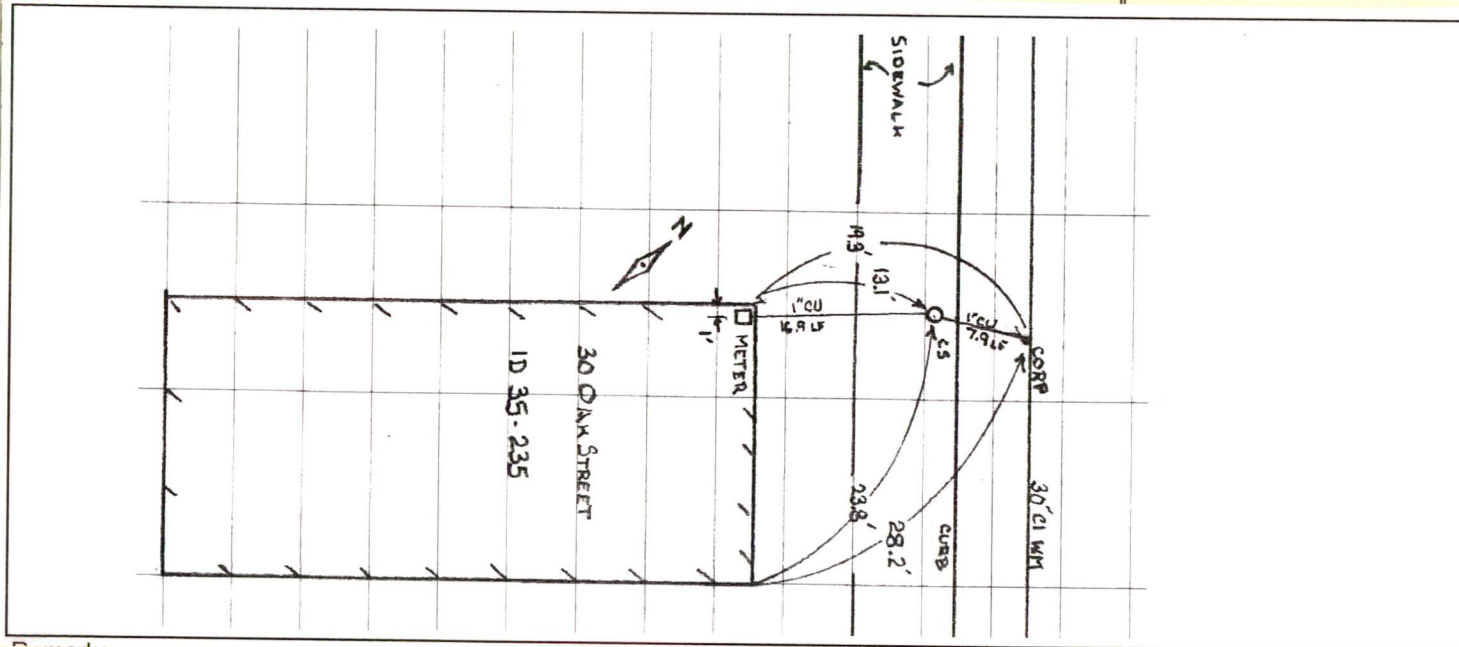
AFT.

REMARKS

1/41

METER HISTORY									
DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST			REMARKS
						Ties:			

Ties:

[illegible]
