

APPLICATION No.: 8727

LOCATION: 29 Hall St

OWNER:

31-313

MEASURES: 05/15/2019 Lead Service Line Replacement
Program, Phase 1, Contractor P Gioioso & Son
Type CU, Diameter 1in, Water pressure 100
Distance from main to curb stop (ft) N/A
Distance from curb stop to meter (ft) 17
Distance from curb face to curb stop (ft) 2
Depth of service (ft) 4
Total length of new pipe installed (ft) 17
Curb stop replaced: no Corporation replaced: no
Ball valve furnished: yes, size 1"

TAP CLEARED

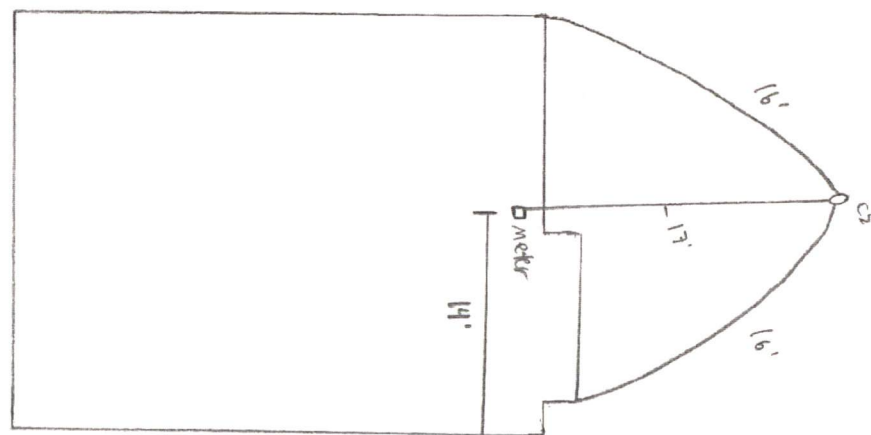
DATE _____

BEF.

AFT.

REMARKS

[illegible]

[illegible]

APPLICATION No.: 8727TAP CLEARED T907-081-12 ✓LOCATION: 29 Hall St.OWNER: Manuel CorreiaMEASURES: $\frac{1}{2}$ " H lead Aug. 21, 1896

S from Thompson St. 93.2 ft.

E from W line Hall St. 7.3 ft.

S from N line house 9.7 ft.

3/19/90: Renewed from main to prop line

Stock: 18 ft. $\frac{3}{4}$ " copper tubing 1- $\frac{3}{4}$ " curb stop1-Caldwell stop box 1- $\frac{3}{4}$ " corporation tap1-4" x $\frac{3}{4}$ " service saddle.=====

June 6, 1995:

S & B Const. renewed service from the newly installed 8" main
to a point 3.6ft Stock supplied & installed by contractor3.6ft $\frac{3}{4}$ " copper tubing 1- $\frac{3}{4}$ x $\frac{3}{4}$ cop-copc plg.comp1- $\frac{3}{4}$ " corporation tap S & B cont. to maintain cut
=====

[illegible]

CHARGE OUTS

[illegible]
