

✓ APPLICATION No.: 8872

LOCATION: 16 Viall St

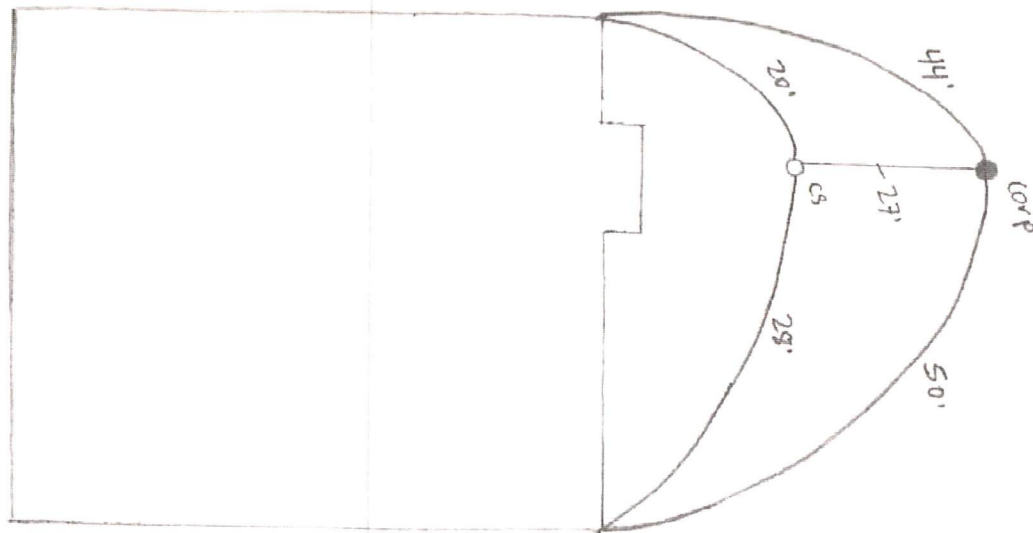
OWNER:

31-313

MEASURES: 4/9/2019 1" Copper Service  
Lead Service Line Replacement Program  
Phase 1, Contractor P Gioioso & Son  
Type CU, Diameter 1in, Water pressure 100  
Distance from curb stop to main (ft) 27  
Distance from curb stop to meter (ft) N/A  
Distance from curb face to curb stop (ft) 2  
Depth of service (ft) 4  
Total length of new pipe installed (ft) 27  
Curb stop replaced: Yes size 1"  
Corporation replaced: No  
Ball valve replaced: NO

TAP CLEARED

[illegible]

[illegible]

APPLICATION No.: 8872

TAP CLEARED 8634-0016

LOCATION: 16 Viall

OWNER: Daniel Reynolds

MEASURES: 5/8"

S from  
W from E  
N from S

Cove ST.  
Viall  
house

285.5 ft.  
9.1 ft.  
7.0 ft.

May 10 , 1960 Renewed from a point 1 ft. inside prop.  
line to inside cellar.

7 ft. - 3/4" Copper tubing

Aug. 18, 1975 Renewed from  $\frac{1}{2}$  ft. outside curb stop to the property line.

9½ ft. - 3/4" Copper tubing

2 wipe joints

3/4" Curb stop

Buffalo Stop Box

8/18/86: Renewed from main to a point 1 ft.

Stock: 1 ft. 3/4" copper tubing 1 - 3/4 x 5/8 lead to cop adapt.xxs

1 - 3/4 x 5/8 Fig. 413

12/21/93: Renewed from main to a point 1.8ft

Stock: 1.8ft 3/4" copper tubing re-used lead-cop adapt.

1-3/4" corporation tap 1-6x3/4 service saddle (smith Blair)

6-22-98 Dug Stop Box could not get in box, Stock: 1 - Caldwell  
Stop Box,

DATE \_\_\_\_\_

BEF.

AFT.

REMARKS

8/18/86:	TAP	REAMED
----------	-----	--------

6/22/98

922/10082

1	1
2	2340

182600002	
-----------	--

7/27/00	
---------	--

2000-0900494

Chapel Exeter

11-19-01

8:30

2001 470 0429



[illegible]

2-22-00 Tap reamed  
11-19-01 Tapreamed
