

APPLICATION No.: 9129

LOCATION: 57 West Rodney French

TAP CLEARED

OWNER:

31-313

MEASURES: N X S Line Brock Ave 7.3 ft
E X W Line W French Ave 10.8 ft
S X N Line House 6.3 ft

4/10/2019 1" Copper Service

Lead Service Line Replacement Program

Phase 1, Contractor P Gioioso & Son

Type CU, Diameter 1in, Water pressure 95

Distance from main to curb stop (ft) 23.3

Distance from curb stop to meter (ft) 32

Distance from curb face to curb stop (ft) 2.4

Depth of service(ft) 4

Total length of new pipe installed (ft) 23.3

Curb stop replaced: Yes size 1"

Corporation replaced: Yes size 1"

Ball valve replaced: No size 3/4"

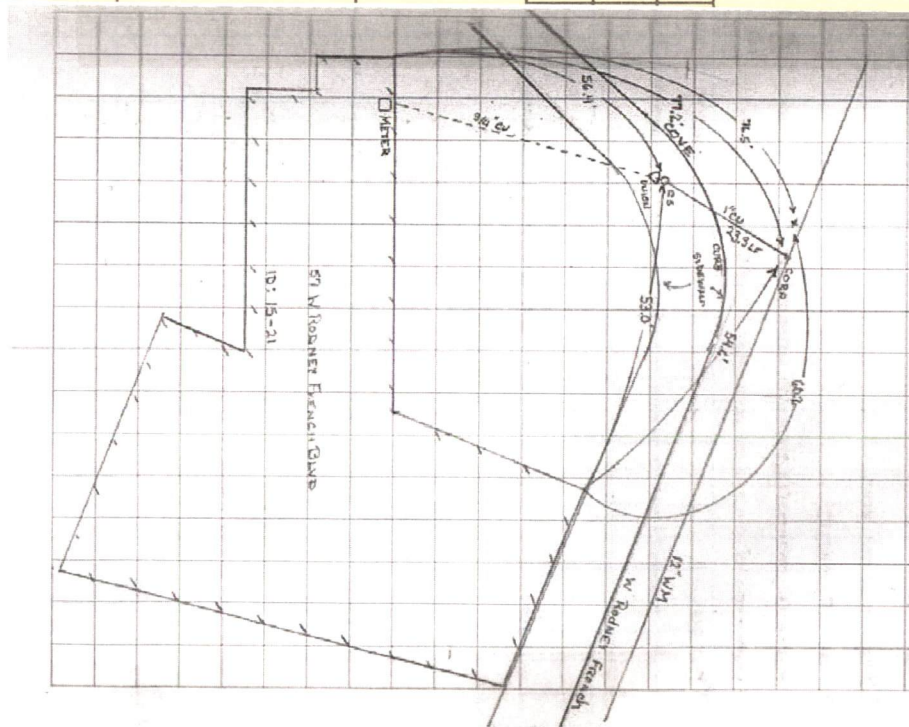
1-3/4 union installed 1LF outside curb stop

DATE

BEF.

AFT.

REMARKS

[illegible]



Aug. 11, 1997 3/4 S.W. for
gas STA.
