

APPLICATION No.: 9290

LOCATION: 197 - 199 Grinnell St

TAP CLEARED

DATE _____

BEF.

AFT.

REMARKS

OWNER:

31-313

MEASURES: E X Orchard St 24.0 ft

24.0 ft

S X N Line Grinnell St 7.0 ft

7.0 ft

| | |
|------------------|--------|
| W X E Line House | 4.5 ft |
|------------------|--------|

4.5 ft

1" Copper Service

09/20/2018 Lead service line replacement program

Phase 1, Contractor P Gioioso & Son

Type CU, Diameter 1in, Water pressure 80

Distance from main to curb stop (ft) 22

Distance from curb stop to meter (ft) 13.1

Distance from curb face to curb stop (ft) 0.8

Depth of service (ft) 4.0

Total length of new pipe installed (ft) 13.1

Curb stop replaced; no size 3/4"


Corporation replaced: size 3/4"

Ball valve furnished: yes size 1"

remarks: 1-3/4" union located 1.0 ft outside
curb stop

[illegible]

6" WM

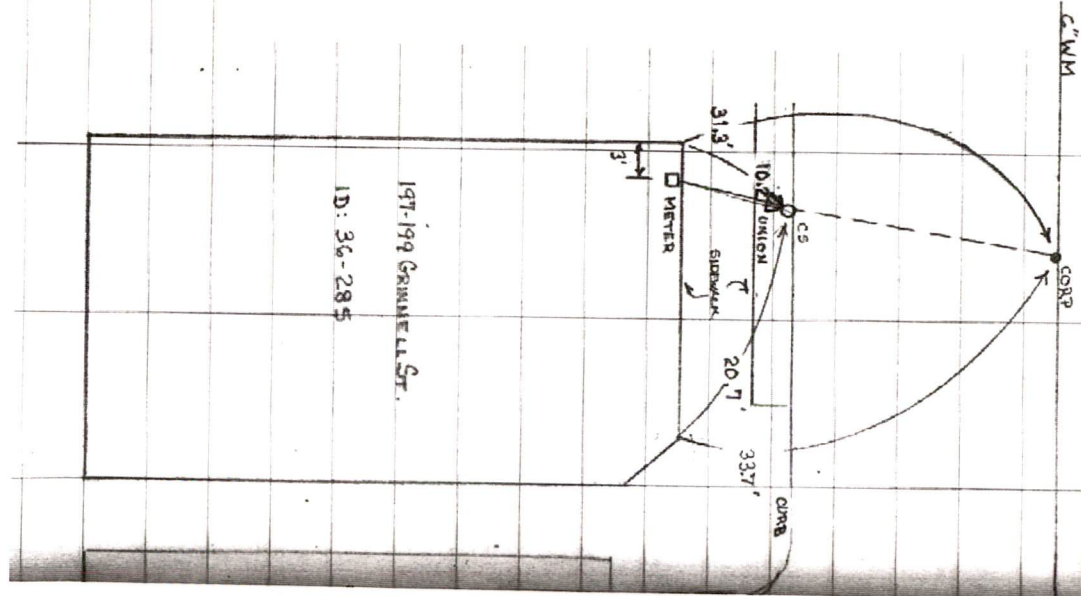

APPLICATION No.: 9290

TAP CLEARED ✓

LOCATION: 199 Grinnell St.

OWNER: Mary Martin

DATE

BEF.

AFT.

REMARKS

9/27/66

reamed

MEASURES: 5/8" H lead Oct. 22, 1897

E from Orchard St. 24.0 ft.

S from N line Grinnell St. 7.0 ft.

W from E line house 4.5 ft.

Sept. 27, 1966 Renewed from main to a point 1 ft. from main
1 ft. of 3/4" copper tubing 5/8" Reused tail piece
1 wiped joint

5/4/06 dug and found copper

[illegible]

CHARGE OUTS

[illegible]
