

APPLICATION No.: 9700

LOCATION: 235 Rivet St

TAP CLEARED

OWNER:

31-313

MEASURES: Jan 26, 1900

E X Crapo St 85.5 ft

S X N Line Rivet St 9.6 ft

E X W Line House 12.5 ft

1" Copper Service

12/11/2018 Lead Service Replacement Program

Phase 1, Contractor P Gioioso & Son

Type CU, Diameter 1in, Water pressure 95 (meter)

Distance from main to curb stop (ft) 24.5

Distance from curb stop to meter (ft) 19.5

Distance from curb face to curb stop (ft) 1

Depth of service (ft) 4

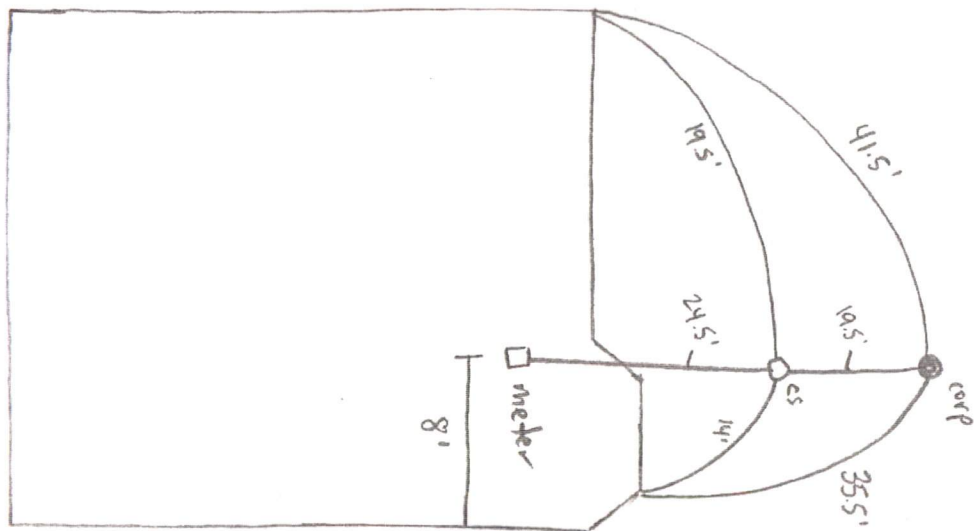
Total length of new pipe installed (ft) 44

Curb stop replaced: Yes size 1"

Corporation replaced: Yes size 1"

Ball valve replaced: Yes size 1"

METER HISTORY

[illegible]

CHARGE OUTS

[illegible]
