

APPLICATION No.: 9705

TAP CLEARED

LOCATION: 24 Morton Court

DATE

BEF.

AFT.

REMARKS

OWNER:

31-313

MEASURES March 2, 1900

N X Cove St 229.0 ft

W X E Line Morton Ct 5.2 ft

S X N Line House 9.0 ft

W X W Line House 12.7 ft

1" Copper Service

11-14-2018: Type CU, Diameter 1in, Water pressure 100

Distance from main to curb stop (ft) 30

Distance from curb stop to meter (ft) 18

Distance from curb face to curb stop (ft) 1.0

Depth of service (ft) 4.0

Total length of new pipe installed (ft) 18

Curb stop replaced: no size 3/4"

Corporation replaced: no size 3/4"


Ball valve furnished: yes size 1"

Remarks: 1-3/4" union installed 1LF outside curb stop

METER HISTORY

DATE	SET OUT	SIZE	MAKE	NUMBER	READING	TEST			REMARKS

CHARGE OUTS

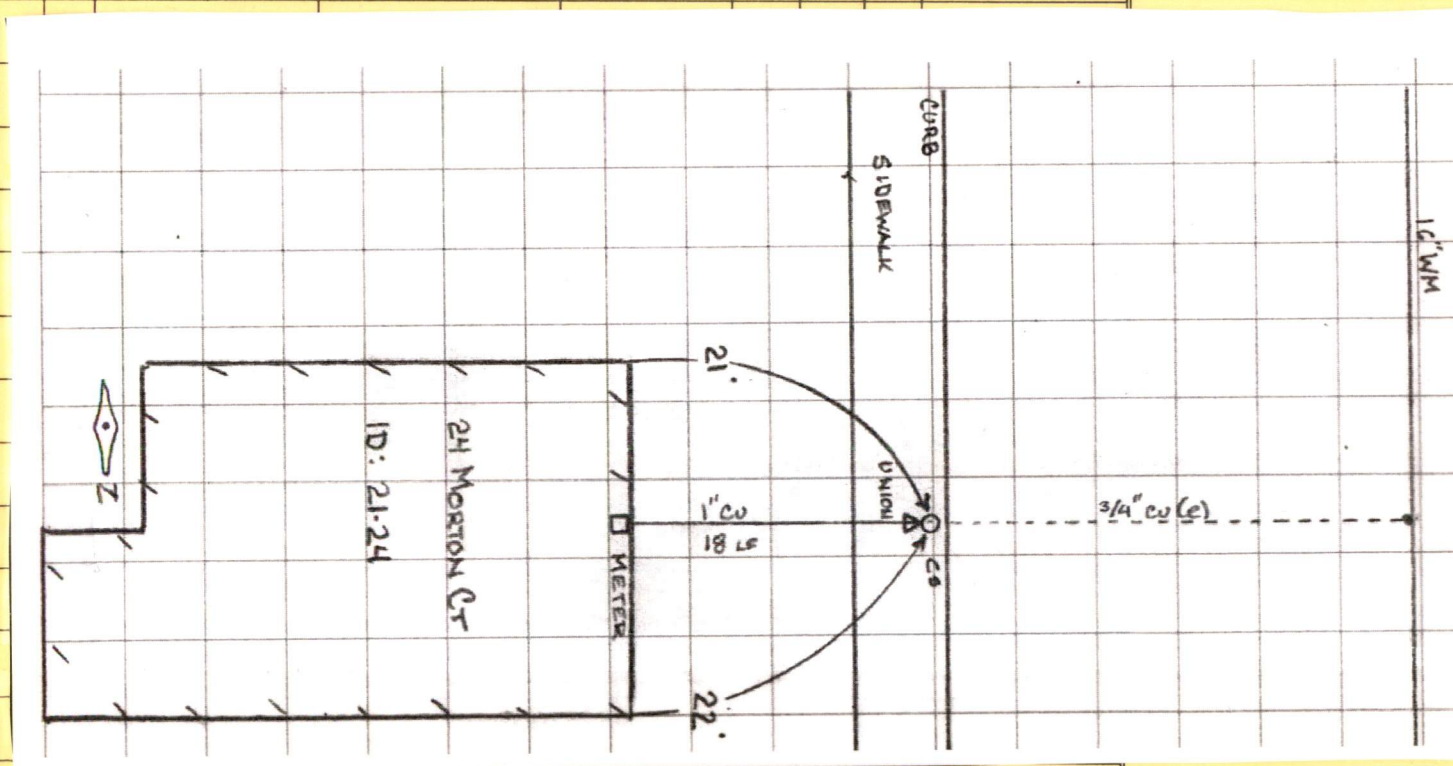

APPLICATION No.: 9705

TAP CLEARED ✓

LOCATION: 24 Morton Court

OWNER: Walter Wisniewski, Et Ux

MEASURES: 1/2" H lead Mar. 2, 1900

N from Cove St. ~~226.7 ft.~~ 229.0 ft.W from E line Morton Ct. ~~6.4 ft.~~ 5.2 ft.S from N line house ~~9.2 ft.~~ 9.0 ft.

W from W line house 12.7 ft.

- - - -
June 1983 JF Kennedy Hwy. Proj. Renewed from the new 16" main to the prop. line.

37 ft. - 3/4" copper tubing 1-3/4" Mueller tap

1-3/4" Mueller curb stop 1-Caldwell stop box

1-3/4" x 5/8" lead-cop. adapt. XS at line

[illegible]

CHARGE OUTS

[illegible]
