

APPLICATION/AGREEMENT

For Trench/Disturbance Permit within the City of New Bedford

Permit #

582-14

Dig Safe #

TO THE MAYOR AND CITY COUNCIL:

DISTURBANCE PERMIT/TRENCH SAFETY PERMIT

Permission is hereby requested to excavate the surface of: City Property and/or

Private Property

Provide Sketch

Location of Work:

166 Williams St

Date

12-14-16

ROADWAY CLOSURES WILL REQUIRE
AUTHORIZATION FROM THE
COMMISSIONER OF PUBLIC
INFRASTRUCTURE. TRAFFIC MANAGEMENT
PLANS MAY BE REQUIRED.

Substantially as per plan annexed, for the purpose of: Repair Concrete

FOR INSPECTION ONLY A 24 HOUR
NOTICE IS REQUIRED AND THE
CONTRACTOR/APPLICANT IS
REQUIRED TO NOTIFY THE D.P.I.
@ 508 979-1550 Press 3 Repair

Work will begin (weather permitting) on: 12/21/16

Work will end (weather permitting) on: 3/21/17

Applicant Name: Kennett Excavator(s) Name:

Company Name: Precision Valley Commnic
of Vermont, LLC

Hoisting Equipment License Number:

Grade:

Expiration Date:

Contact Number: 1-802-885-9317

Name & Contact Number of Insurer: Willis of Pennsylvania

DIC 1-877-945-7378

Competent Person on Work Site:


APPROVED BY: Dan M. Smith

DATE: 12/14/16

TITLE:

Chief of the Works

This permit shall be posted at the work site, and shall remain until the work is completed. It is subject to inspection at all times.



INVOICE WORK ORDER DATA SHEET

DATE: 12/2/2016
CONTRACTOR: PVC

MANAGER: Doug Carr
STREET: 440 Myles Standish Blvd.
STATE: MA
PHONE #: 508-884-2367
Engineer: Fred Cabral
CITY: Taunton
Zip Code: 02780

PROJECT NAME: 166 William Street Repair
TOWN: New Bedford
CONTACT: Manny Silva
CONTACT NUMBER: 508-509-5461
COMPLETION DATE: 12/9/2016

EXPENDITURE TYPE: Expense
PROJECT NUMBER: PRNB1663

DESCRIPTION OF WORK TO BE PERFORMED:

Please provide material and labor to remove and replace concrete sidewalk panels in front of 166 William Street. Police detail is needed.
This work has been requested by Manny Silva at the DPL.

ANY HOURLY WORK DONE ON PROJECT MUST BE APPROVED BY PC PRIOR TO BEING WORKED.


ALL WORK TO BE DONE TO COMCAST CONSTRUCTION MANUAL SPECIFICATIONS // CHECK YOUR STOCK

18" cover depth unless otherwise required in the permit.
When requested sleeve the road with 3" conduit and then pull cable con.
Dig 12" wide or less depending on the amount of conduits being installed.
Flow fill is not placed under sidewalks unless required
Flow fill (slurry) is paid by line item. (not line item and material) Back up of material is required
When required, dig and flow fill 12" wide then cut back 6" either side for a 24" wide cut and restoration.
All Commercial work requires 3" conduit at a minimum
Pictures should be taken before and after work. Depth of trench should be illustrated. (E-mail pictures)
Notification of completed work must be sent within 24 Hrs or sooner. Phone message followed up by e-mail or just e-mail

- There may be non-member utilities in the area that you need to notify.
- Electric and other companies may not mark lines they don't own or maintain. You may want to contact them for more information.

Request Number: 20164907453 Date 12/09/2016 Time 11:34		
Latitude: Longitude:		
State: MASSACHUSETTS Municipality: NEW BEDFORD		
Address / Intersection: 164-166 WILLIAM ST		
Nearest Cross Street 1: N 6TH ST Nearest Cross Street 2: 8TH ST		
Additional Information:		
Nature Of Work: EXCAVATION FOR COMCAST		
Area Of Work: REPLACING THE CONCRETE SLAB AT #164 AND #166		
Area Is Premarked: Y Start Date: 12/14/2016 Start Time: 11:35		
Caller: KENNY MONIZ Title: PROJECT MANAGER Return Call: 7-7		
Phone#: 978-551-1012 Fax#: 978-663-9400 Alt. Phone#:		
Email Address: DIGSAFE@PVC2.COM		
Contractor: PRECISION VALLEY COMMUNICATIONS		
Address: 144A RANGWAY RD City: BILLERICA State: MA Zip: 01862		
Excavator Doing Work: ANDERSON CONSTRUCTION, PRECISION VALLEY COMM		
Member Utility List		
Code	Abbreviation	Name
CN	NSTREL	NSTAR ELECTRIC-COM
CP	NSTGAS	NSTAR GAS
E115	ESINET	ESI ADVANCED WIRELESS NETWORKS, LLC
HK	COMCAS	COMCAST - PEMBROKE
WW	VERIZN	VERIZON
ON	ONTARG	ON TARGET LOCATING
RJ	VERIZN	VERIZON

SKETCH OF PROPOSED STREET OPENING

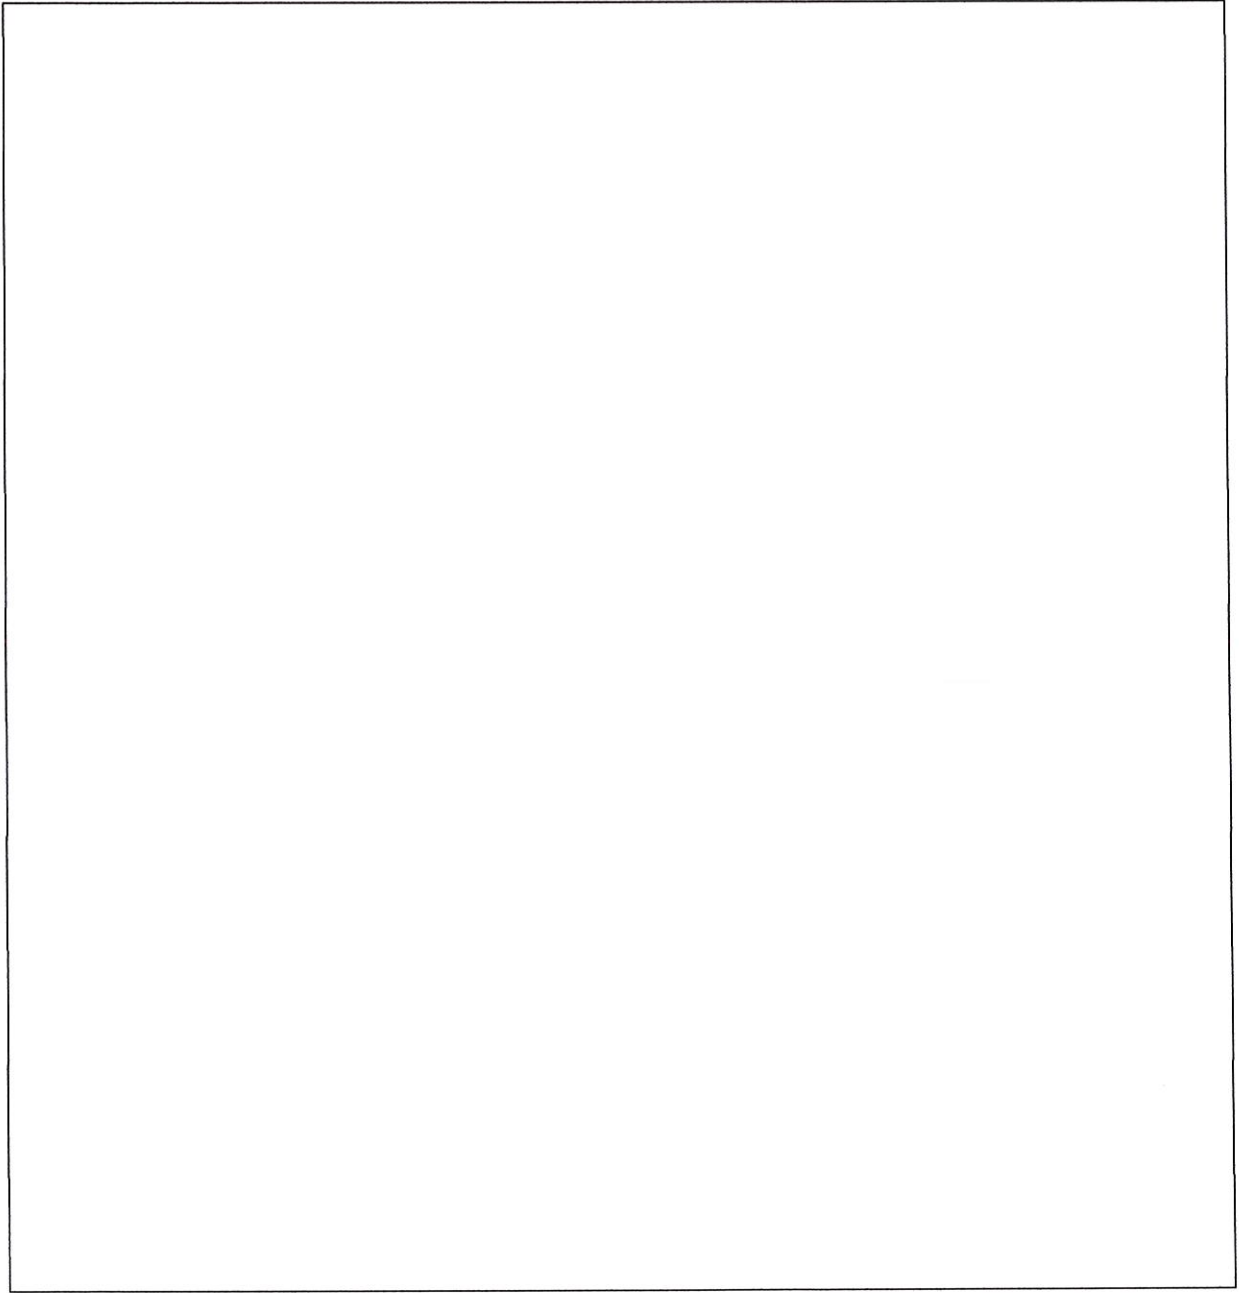

Please show:

- North Arrow
- Sketch of property
- Sketch of buildings
- Location of existing utilities
- Location of proposed utilities
- Patch location
- Street Names
