

Tel. 997-2811

Acushnet Co.

754 Belleville

12/15/88

by Stuart K. Mills, Jr. N.B. Ma 02745

#31277 S.S. S. Barnet Blvd. W x N.B. city line. 133

Please install 6" ductile to supply a mfg. facility.
from S. Barnet Blvd. Meter in pit. Nota Construction.

Measures of 8" Gate Valve, Mech.

W x W line J. Vertente Blvd.

1887.0 ft.

N x S line S. Barnet Blvd.

29.6 ft.

Work done Jan. 9 & 10, 1989

Insp.....\$ 10.78

Turn on charge.....\$ 25.00

\$ 35.78

Nota Const. supplied & installed stock.

Service installed in following order:

Beginning at hydrant tee southerly:- into property under drainage trench.

2 ft. - 8" ductile pipe

1 - 8" 45° Bend, mech. (down) (2'6" S x hyd. tee)

2 ft. - 8" ductile pipe

1 - 8" 45° Bend, mech. (4' S x hyd. tee)

14 ft. - 8" ductile pipe (under trench)

1 - 8" 45° Bend, mech (up)

3 ft. - 8" ductile pipe

1 - 8" 45° Bend, Mech. (21.6 ft. S x hyd. tee)


15 ft. - 8" ductile pipe

1 - 8" 90° Bend, Mech. (36.6 ft. S x hyd. tee)

5 ft.- 8" ductile pipe (west x bend)

1 - = 8" x 6" Reducer, mech.

31277-8"
RED-
6"

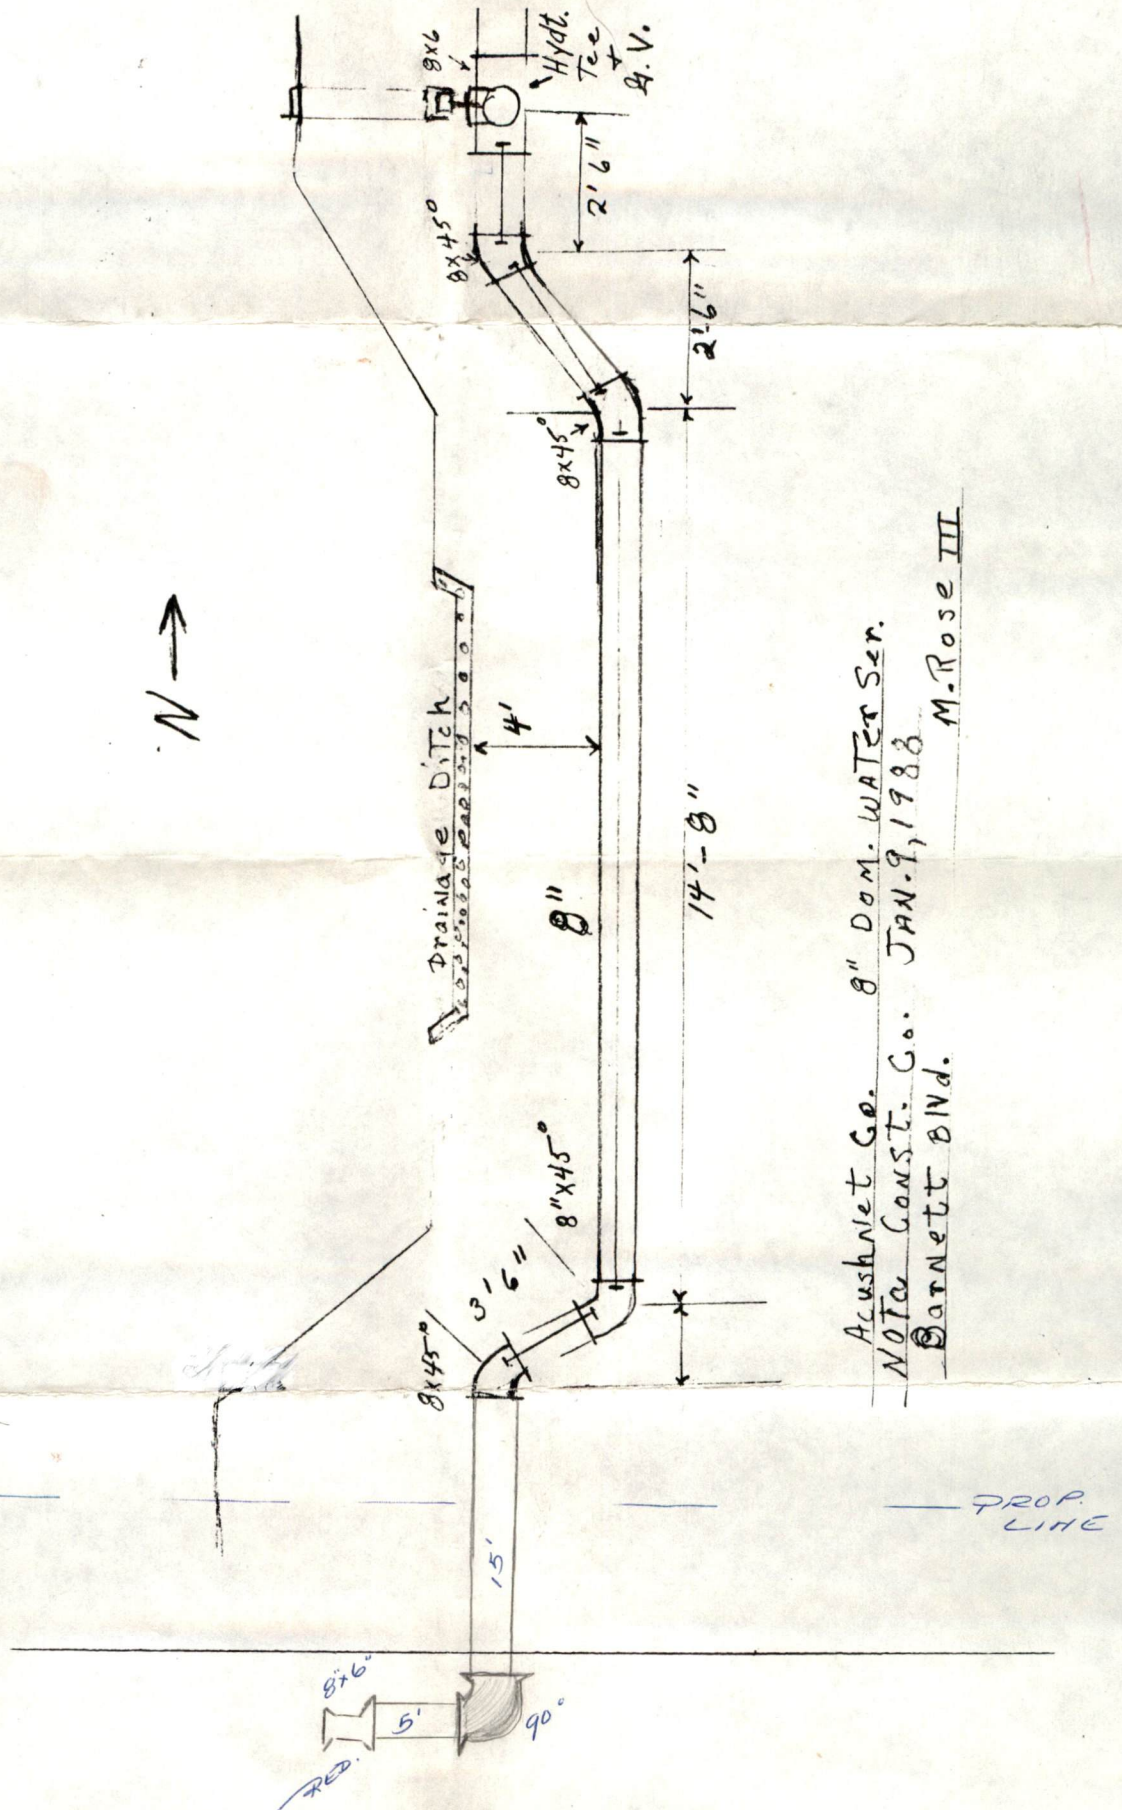

Acushnet Co. 8" DOM. WATER SER.
NOTAR CONST. CO. JAN. 9, 1988
BARNETT BND. M. ROSE III

PROP.
LINE
