

Water St.

Cove St.


to

Gifford St

P14 2946

PART	KIND AND THICKNESS					JOINTS	AREA	COST PER SQ. YD.	LAID BY	YEAR	NOTE BOOK	REMARKS
	TOP	CUSHION		BASE								
24' WIDE												
E. & W. of track	Stone block	Sand	Concrete					3.85	City	1909		Blocks laid on side Over.
Full width	Wood Block 3 1/2"	1-3 Mortar 1/2"	1-4-4 Concrete	Pitch & Sand.					City	1916	334-9	not completed. See back of card for detail of construction
" "	Wood Block 3 1/2"	1-3 Mortar 1/2"	"	Pitch & Sand					City	1917		Removed wood block.
Full width	Warrenite 2"		Old conc. Bit. binder 2 1/2"						Warren Bros.	1935		
" "	Bit. Conc. 2"	Laid over	old pavement & car track						D. P. W.	1947		

Library Bureau K8168

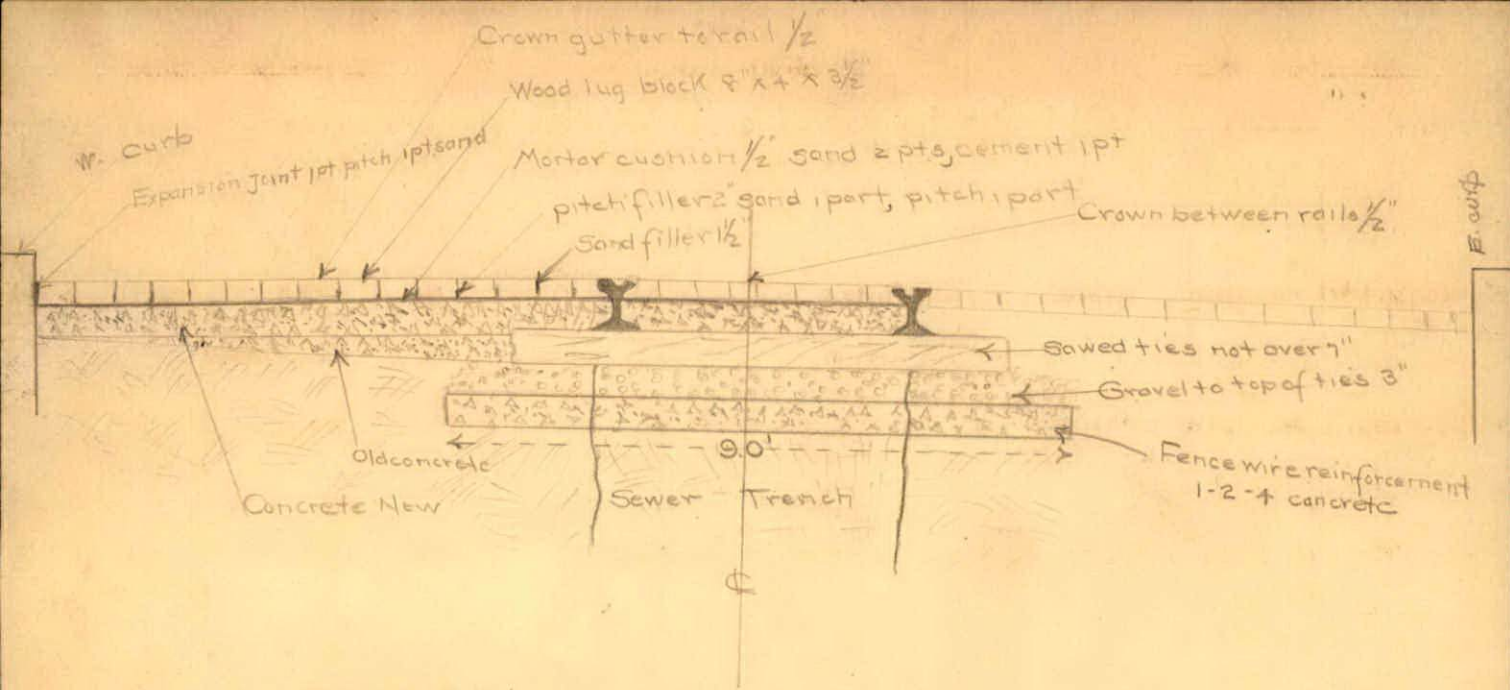

Section from Cove St. to N. L. Delano St.
