SERVICE TO
Kleeden Mfg. Co.

APR. 23 '14
Smith
Lemos

68

Plotted

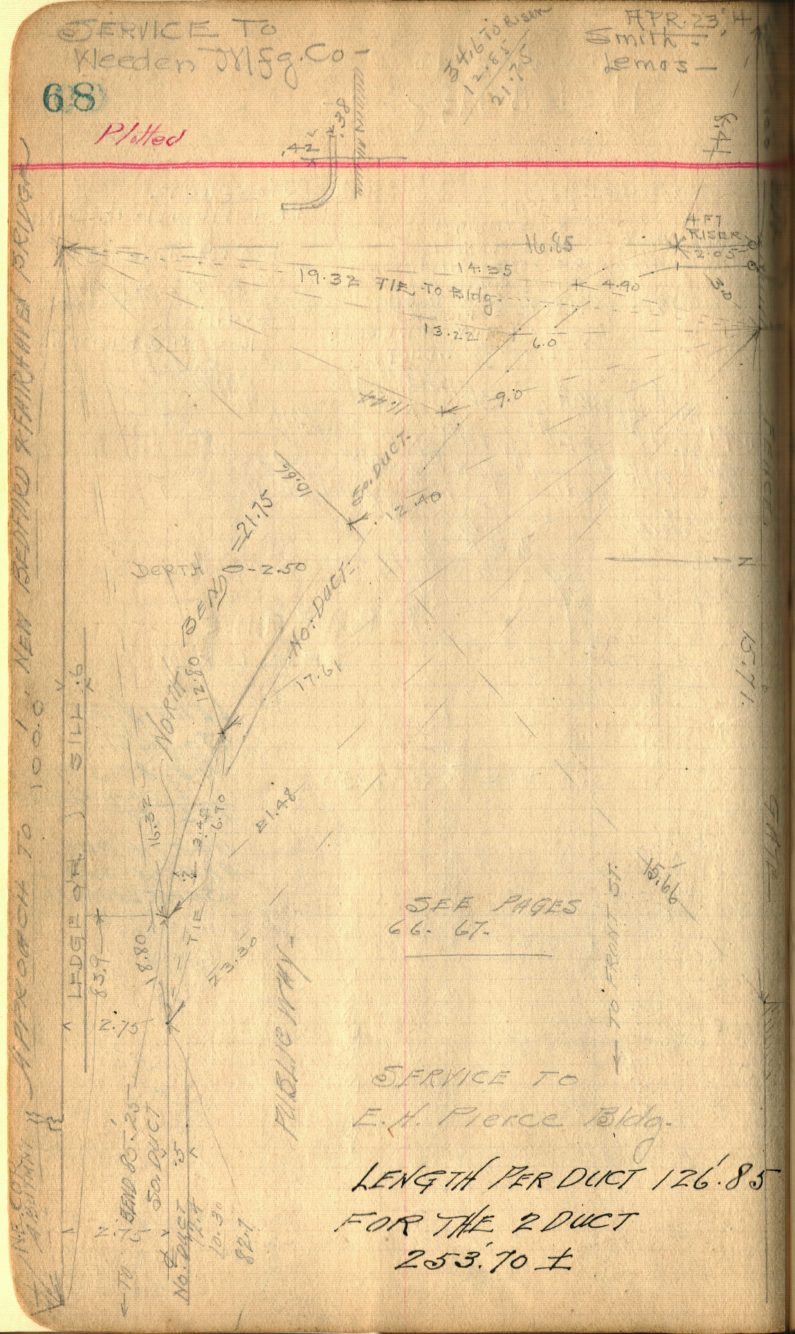

LENGTH PER DUCT 126'.85
FOR THE 2 DUCT
253.70 ±

SERVICE TO RISER POLE
NR. NE. COR. WILLIAM AND
COUNTY STS. 2-3" FIBRE DUCTS.

APR. 23 '14
Smith
Lemos

69

Plotted

29.85
3.35 ± M.H. COVER TO N. NGH M.H.
26.50 = Length of 3" FIBRE
4.00 = 3" GALV. IRON RISER
30.50 PER DUCT. ENTERED ON TRACING.
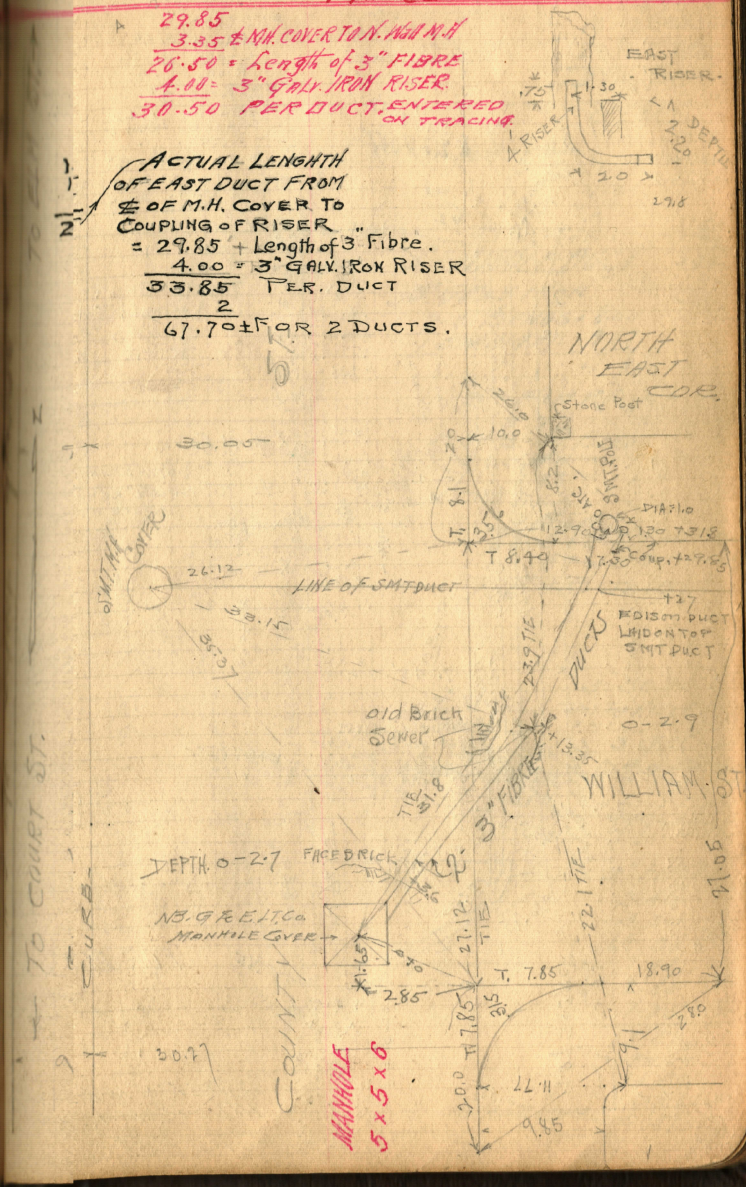
ACTUAL LENGTH OF EAST DUCT FROM ℄ OF M.H. COVER TO COUPLING OF RISER
= 29.85 + Length of 3" Fibre.
4.00 = 3" GALV. IRON RISER
33.85 PER. DUCT
2
67.70 ± FOR 2 DUCTS.
